

ROADWAY REDEVELOPMENT
BID AWARD

Michigan Office
6340 Sims Drive
Sterling Heights, Michigan 48313
Office: 586-268-2090
Fax: 586-268-7099



SE Florida Office
1801 NW 18th Street
Pompano Beach, FL 33069
Office: 954-972-8104
Fax: 954-972-8108

February 4th, 2021

Ms. Marilane Lima, MMC Indian Creek Village
9080 Bay Drive
Indian Creek Village, FL 33154

Re: Request for Proposals #2020-01
Roadway Redevelopment Project

Dear Ms. Lima,

Please accept this as our letter of interest to exceed Village expectations on the above referenced Roadway Redevelopment Project. We understand you are considering a competitive bid and that price alone may not be the deciding factor. Giannetti is a seventy (75) five-year family owned construction business uniquely qualified to earn your consideration on this challenging project. We possess vast experience with Road building, Pipeline installation and Materials handling to remote locations. In fact, we have installed work on your Island! On or about 2001 Giannetti installed fourteen (14) Catch Basins, Storm Drainage and conducted Injection Well Tie ins at 14 Indian Creek Island Road. If he is still at the residence we defer to His Excellency, the Ambassador to Belgium who seemed quite impressed with the scope and expediency of our effort! More recently, we have successfully completed "similar" work which will insure against any "learning curve" which might otherwise occur during transition to this project.

We present the following examples of work successfully completed by Giannetti within the past five (5) years which are quite analogous to the challenges presented on your project.

1. Singer Island Riviera Bch \$11M "Award Winning" New Concrete Road, Sewer & Drainage
Singer Island is an exclusive Nautical subdivision in a City with a Rich "Ocean Going" tradition
2. Jupiter Inlet Colony \$12M New Roadway Water Sewer Drainage (168 Homes)
With only one way in-and-out; this "exclusive" Ocean Front community was served with Water, Sewer, Drainage and Roadway Construction in a non-disruptive manner to the ingress and egress patterns within the community. We performed our work with minimal impact to, or interaction with, the residents.
3. FCAA Inter-islands \$42M Pump Stations, Low Pressure Gravity and Roadway Construction in an Environmentally Sensitive area rich with wildlife and protected vegetation. We have installed over six (600) hundred grinder lift station installations within the Florida Keys at various remote and dedicated locations.

The key features of your project which are highly compatible with our most practiced core competencies include:

- Work in a community with only one (1) way in or out. This requires absolute sensitivity to the needs of the residents on a Day-to-Day, as well as, intraday basis.
- Work requiring an expeditious combination of drainage and roadway construction in an exclusive surrounding where every activity is High visibility while the residents command a great deal of sway with the

entity overseeing construction. We offer extensive communication, a private website, and social media alerts (if subscribed and only by authorized personnel) of each construction activity in Real Time.

- Work where there is coastal and tidal influence impacting ground conditions and water table
- Work where there must be recognized safety protocol, no tolerance for incidents or accidents. We hold safety first as one of our most revered core values. Giannetti has a Safety Mod Value in the low .8's which should prove to be the best of all respondents to this offering. This, an often taken for granted attribute, ensures project continuity and diminished impact to the communities in which we serve.

Finally, we understand that there are contractually six hundred (600) days allowed for completion of this project. We also understand that, given the value and prestige of the properties being served by this project that there is value to "early completion". Our schedule, made part of this proposal, offers an early completion.

Respectfully submitted,

GIANNETTI CONTRACTING CORPORATION

A handwritten signature in black ink, appearing to read "Richie Gibbs", is written over a long, thin horizontal line that spans across the width of the signature area.

Richie Gibbs, President

*Indian Creek Village
Roadway Redevelopment Project*

Project Approach

Giannetti Contracting will perform the Roadway Redevelopment Project with the Village and its residents in mind. After Contract Award, Giannetti would immediately proceed with the submittals and permitting. Soon after, Giannetti would proceed with mobilization, erosion control, tree protection, and exploration of existing utilities.

Giannetti will closely monitor all construction related traffic crossing the bridge. We will insure the sixteen ton weight limit isn't exceeded. We will utilize five cubic yard dump trucks for all hauling to the island. All concrete trucks to the island will be half loads. All large equipment and materials will be shipped to the island by barge.

The entire project will be broken up into eleven sections. The first section will begin at the Northwest corner of project and will be broken into segments of seven hundred and fifty to one thousand linear feet sections.

Each of the eleven sections will have similar phasing. The first item of each phase would be road demolition followed by the temporary road installation. Giannetti would utilize the removed roadway asphalt and base to construct the temporary road on the golf course side of the roadway. We would install the temporary road to keep the flow of traffic moving for the residents while minimizing the impacts on the golf course. The temporary road would be adjacent to the new proposed roadway. After temporary road is constructed, Giannetti would continue with the drainage installation followed by the low pressure installation, water service connections, and electrical conduit installation. Once all the underground is complete, Giannetti would start the road reconstruction and also move the pipe crew to the next phase to start drainage installation. After the road subgrade is installed, Giannetti would proceed to install the concrete curbing followed by the limerock road base installation and 1st lift of asphalt. Once the 1st asphalt lift is installed, Giannetti would remove the temporary road and restore the sod where the temporary road was located. Any irrigation damaged during construction will be repaired ASAP.

After the eleven sections are complete, Giannetti would proceed with light pole installation, the rubber walkway installation, landscaping, final asphalt lift, striping, and signage.

After project scope is complete, Giannetti will demobilize equipment, remove any material left from project, and restore storage yards provided by Village on island to preconstruction condition.

Giannetti expects to complete this project within thirteen months.

Giannetti is willing to change elements of the project approach to accommodate the Village and/or residents. We will work as a team with the owner and its residents.

Proposed project schedule is attached.

INDIAN CREEK VILLAGE

Construction Schedule

04-Feb-21 08:11

Activity ID	Activity Name	Planned Start	Planned Finish	Original Duration	Total Float	Activity % Complete	2021				2022			
							Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
ICV INDIAN CREEK VILLAGE														
ICV.1 GENERAL REQUIREMENTS														
A1000	CONTRACT AWARD	01-Apr-21	28-Apr-22	281	168	0%								
A1010	SHOP DRAWING SUBMITTAL AND REVIEW	01-Apr-21	29-Apr-21	21	428	0%								
A1020	PERMITTING	01-Apr-21	01-Apr-21	1	0	0%								
A1030	MOBILIZATION	02-Apr-21	29-Apr-21	20	168	0%								
A1040	EROSION CONTROL / NPDES DEVICES	02-Apr-21	15-Apr-21	10	173	0%								
A1050	TREE PROTECTION	16-Apr-21	22-Apr-21	5	433	0%								
A1060	EXPLORATION OF EXISTING UTILITIES	16-Apr-21	22-Apr-21	5	173	0%								
ICV.2 BEGINNING OF THE ICV CONSTRUCTION														
ICV.2.01	HOUSE # 1 THRU # 5, STA:422+00 -> 432+00	30-Apr-21	16-Feb-22	209	168	0%								
B1000	ROAD MILLING/DEMO	30-Apr-21	05-Jul-21	47	205	0%								
B1010	TEMPORARY ROAD INSTALLATION	30-Apr-21	03-May-21	2	168	0%								
B1020	DRAINAGE INSTALLATION	04-May-21	05-May-21	2	168	0%								
B1030	LOW PRESSURE INSTALLATION AND TESTING	06-May-21	19-May-21	10	168	0%								
B1040	WATER SERVICES CONNECTIONS	20-May-21	26-May-21	5	205	0%								
B1050	ELECTRICAL CONDUIT INSTALLATION	20-May-21	25-May-21	4	206	0%								
B1060	ROAD SUBGRADE INSTALLATION	20-May-21	26-May-21	5	168	0%								
B1070	CONCRETE CURBING AND DRIVEWAYS	27-May-21	02-Jun-21	5	205	0%								
B1080	ROAD LIMEROCK INSTALLATION/GRADING	03-Jun-21	14-Jun-21	8	205	0%								
B1090	PAVING 1ST LIFT OF ASPHALT	15-Jun-21	24-Jun-21	8	205	0%								
B1100	REMOVAL OF TEMPORARY ROAD	25-Jun-21	28-Jun-21	2	205	0%								
B1110	SOD INSTALLATION	29-Jun-21	30-Jun-21	2	205	0%								
ICV.2.02	HOUSE # 6 THRU # 10, STA:432+00 -> 442+00	01-Jul-21	05-Jul-21	3	205	0%								
C1000	ROAD MILLING/DEMO	27-May-21	30-Jul-21	47	311	0%								
C1010	TEMPORARY ROAD INSTALLATION	27-May-21	28-May-21	2	168	0%								
C1020	DRAINAGE INSTALLATION	31-May-21	01-Jun-21	2	168	0%								
C1030	LOW PRESSURE INSTALLATION AND TESTING	02-Jun-21	15-Jun-21	10	168	0%								
C1040	WATER SERVICES CONNECTIONS	16-Jun-21	22-Jun-21	5	311	0%								
C1050	ELECTRICAL CONDUIT INSTALLATION	16-Jun-21	21-Jun-21	4	312	0%								
C1060	ROAD SUBGRADE INSTALLATION	16-Jun-21	22-Jun-21	5	168	0%								

Run Date February 3, 2021 as of April 1, 2021

Final Completion Date April 28, 2022

Project Completion: 0%

Start Date April 1, 2021

Construction Start Date April 30, 2021

1 of 6

INDIAN CREEK VILLAGE ROADWAY REDEVELOPMENT PROJECT

ENGINEER: STANTEC, CORAL GABLES FL

GIANNETTI CONTRACTING PROJECT No F-XXX


Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

INDIAN CREEK VILLAGE

Construction Schedule

04-Feb-21 08:11

Activity ID	Activity Name	Planned Start	Planned Finish	Original Duration	Total Float	Activity % Complete	2021				2022									
							Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4				
C1070	CONCRETE CURBING AND DRIVEWAYS	30-Jun-21	09-Jul-21	8	311	0%														
C1080	ROAD LIMEROCK INSTALLATION/GRADING	12-Jul-21	21-Jul-21	8	311	0%														
C1090	PAVING 1ST LIFT OF ASPHALT	22-Jul-21	23-Jul-21	2	311	0%														
C1100	REMOVAL OF TEMPORARY ROAD	26-Jul-21	27-Jul-21	2	311	0%														
C1110	SOD INSTALLATION	28-Jul-21	30-Jul-21	3	311	0%														
ICV 2.03 HOUSE # 11 THRU # 14, STA.442+00 -> 452+00		23-Jun-21	26-Aug-21	47	292	0%														26-Aug-21, ICV.2.03
D1000	ROAD MILLING/DEMO	23-Jun-21	24-Jun-21	2	168	0%														
D1010	TEMPORARY ROAD INSTALLATION	25-Jun-21	28-Jun-21	2	168	0%														
D1020	DRAINAGE INSTALLATION	29-Jun-21	12-Jul-21	10	168	0%														
D1030	LOW PRESSURE INSTALLATION AND TESTING	13-Jul-21	19-Jul-21	5	292	0%														
D1040	WATER SERVICES CONNECTIONS	13-Jul-21	16-Jul-21	4	293	0%														
D1050	ELECTRICAL CONDUIT INSTALLATION	13-Jul-21	19-Jul-21	5	168	0%														
D1060	ROAD SUBGRADE INSTALLATION	20-Jul-21	26-Jul-21	5	292	0%														
D1070	CONCRETE CURBING AND DRIVEWAYS	27-Jul-21	05-Aug-21	8	292	0%														
D1080	ROAD LIMEROCK INSTALLATION/GRADING	06-Aug-21	17-Aug-21	8	292	0%														
D1090	PAVING 1ST LIFT OF ASPHALT	18-Aug-21	19-Aug-21	2	292	0%														
D1100	REMOVAL OF TEMPORARY ROAD	20-Aug-21	23-Aug-21	2	292	0%														
D1110	SOD INSTALLATION	24-Aug-21	26-Aug-21	3	292	0%														
ICV 2.04 HOUSE # 15 THRU # IC COUNTY CLUB, STA.452+00 ->		20-Jul-21	22-Sep-21	47	273	0%														21-Sep-21, ICV.2.04
E1000	ROAD MILLING/DEMO	20-Jul-21	21-Jul-21	2	168	0%														
E1010	TEMPORARY ROAD INSTALLATION	22-Jul-21	23-Jul-21	2	168	0%														
E1020	DRAINAGE INSTALLATION	26-Jul-21	06-Aug-21	10	168	0%														
E1030	LOW PRESSURE INSTALLATION AND TESTING	09-Aug-21	13-Aug-21	5	273	0%														
E1040	WATER SERVICES CONNECTIONS	09-Aug-21	12-Aug-21	4	274	0%														
E1050	ELECTRICAL CONDUIT INSTALLATION	09-Aug-21	13-Aug-21	5	168	0%														
E1060	ROAD SUBGRADE INSTALLATION	16-Aug-21	20-Aug-21	5	273	0%														
E1070	CONCRETE CURBING AND DRIVEWAYS	23-Aug-21	01-Sep-21	8	273	0%														
E1080	ROAD LIMEROCK INSTALLATION/GRADING	02-Sep-21	13-Sep-21	8	273	0%														
E1090	PAVING 1ST LIFT OF ASPHALT	14-Sep-21	15-Sep-21	2	273	0%														
E1100	REMOVAL OF TEMPORARY ROAD	16-Sep-21	17-Sep-21	2	273	0%														
E1110	SOD INSTALLATION	20-Sep-21	22-Sep-21	3	273	0%														
ICV 2.05 HOUSE # 16 THRU # 20, STA.462+00 -> 472+00		16-Aug-21	19-Oct-21	47	254	0%														19-Oct-21, ICV.2.05



Run Date February 3, 2021 as of April 1, 2021
 Final Completion Date April 28, 2022
 Project Completion: 0%
 Start Date April 1, 2021
 Construction Start Date April 30, 2021

2 of 6
INDIAN CREEK VILLAGE ROADWAY REDEVELOPMENT PROJECT
 ENGINEER: STANTEC, CORAL GABLES FL
 GIANNETTI CONTRACTING PROJECT No F-XXX


Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

INDIAN CREEK VILLAGE

Construction Schedule

04-Feb-21 08:11

Activity ID	Activity Name	Planned Start	Planned Finish	Original Duration	Total Float	Activity % Complete	2021				2022										
							Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4					
F1000	ROAD MILLING/DEMO	16-Aug-21	17-Aug-21	2	168	0%															
F1010	TEMPORARY ROAD INSTALLATION	18-Aug-21	19-Aug-21	2	168	0%															
F1020	DRAINAGE INSTALLATION	20-Aug-21	02-Sep-21	10	168	0%															
F1030	LOW PRESSURE INSTALLATION AND TESTING	03-Sep-21	09-Sep-21	5	254	0%															
F1040	WATER SERVICES CONNECTIONS	03-Sep-21	08-Sep-21	4	255	0%															
F1050	ELECTRICAL CONDUIT INSTALLATION	03-Sep-21	09-Sep-21	5	168	0%															
F1060	ROAD SUBGRADE INSTALLATION	10-Sep-21	16-Sep-21	5	254	0%															
F1070	CONCRETE CURBING AND DRIVEWAYS	17-Sep-21	28-Sep-21	8	254	0%															
F1080	ROAD LIMEROCK INSTALLATION/GRADING	29-Sep-21	08-Oct-21	8	254	0%															
F1090	PAVING 1ST LIFT OF ASPHALT	11-Oct-21	12-Oct-21	2	254	0%															
F1100	REMOVAL OF TEMPORARY ROAD	13-Oct-21	14-Oct-21	2	254	0%															
F1110	SOD INSTALLATION	15-Oct-21	19-Oct-21	3	254	0%															
ICV.2.06 HOUSE # 21 THRU # 26, STA:472+00 -> 482+00							47	235													
G1000	ROAD MILLING/DEMO	10-Sep-21	13-Sep-21	2	168	0%															
G1010	TEMPORARY ROAD INSTALLATION	14-Sep-21	15-Sep-21	2	168	0%															
G1020	DRAINAGE INSTALLATION	16-Sep-21	29-Sep-21	10	168	0%															
G1030	LOW PRESSURE INSTALLATION AND TESTING	30-Sep-21	06-Oct-21	5	235	0%															
G1040	WATER SERVICES CONNECTIONS	30-Sep-21	05-Oct-21	4	236	0%															
G1050	ELECTRICAL CONDUIT INSTALLATION	30-Sep-21	06-Oct-21	5	168	0%															
G1060	ROAD SUBGRADE INSTALLATION	07-Oct-21	13-Oct-21	5	235	0%															
G1070	CONCRETE CURBING AND DRIVEWAYS	14-Oct-21	25-Oct-21	8	235	0%															
G1080	ROAD LIMEROCK INSTALLATION/GRADING	26-Oct-21	04-Nov-21	8	235	0%															
G1090	PAVING 1ST LIFT OF ASPHALT	05-Nov-21	08-Nov-21	2	235	0%															
G1100	REMOVAL OF TEMPORARY ROAD	09-Nov-21	10-Nov-21	2	235	0%															
G1110	SOD INSTALLATION	11-Nov-21	15-Nov-21	3	235	0%															
ICV.2.07 HOUSE # 27 THRU # 31, STA:482+00 -> 492+00							47	216													
H1000	ROAD MILLING/DEMO	07-Oct-21	08-Oct-21	2	168	0%															
H1010	TEMPORARY ROAD INSTALLATION	11-Oct-21	12-Oct-21	2	168	0%															
H1020	DRAINAGE INSTALLATION	13-Oct-21	26-Oct-21	10	168	0%															
H1030	LOW PRESSURE INSTALLATION AND TESTING	27-Oct-21	02-Nov-21	5	216	0%															
H1040	WATER SERVICES CONNECTIONS	27-Oct-21	01-Nov-21	4	217	0%															
H1050	ELECTRICAL CONDUIT INSTALLATION	27-Oct-21	02-Nov-21	5	168	0%															



Run Date February 3, 2021 as of April 1, 2021
 Final Completion Date April 28, 2022
 Project Completion: 0%
 Start Date April 1, 2021
 Construction Start Date April 30, 2021

3 of 6
INDIAN CREEK VILLAGE ROADWAY REDEVELOPMENT PROJECT
 ENGINEER: STANTEC, CORAL GABLES FL
 GIANNETTI CONTRACTING PROJECT No F-XXX

Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

INDIAN CREEK VILLAGE

Construction Schedule

04-Feb-21 08:11

Activity ID	Activity Name	Planned Start	Planned Finish	Original Duration	Total Float	Activity % Complete	2021				2022									
							Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4				
H1060	ROAD SUBGRADE INSTALLATION	03-Nov-21	09-Nov-21	5	216	0%														
H1070	CONCRETE CURBING AND DRIVEWAYS	10-Nov-21	19-Nov-21	8	216	0%														
H1080	ROAD LIMEROCK INSTALLATION/GRADING	22-Nov-21	01-Dec-21	8	216	0%														
H1090	PAVING 1ST LIFT OF ASPHALT	02-Dec-21	03-Dec-21	2	216	0%														
H1100	REMOVAL OF TEMPORARY ROAD	06-Dec-21	07-Dec-21	2	216	0%														
H1110	SOD INSTALLATION	08-Dec-21	10-Dec-21	3	216	0%														
ICV 2.08	HOUSE # 32 THRU # 35, STA: 492+00 -> 499+00	03-Nov-21	06-Jan-22	47	197	0%														06-Jan-22, ICV
I1000	ROAD MILLING/DEMO	03-Nov-21	04-Nov-21	2	168	0%														
I1010	TEMPORARY ROAD INSTALLATION	05-Nov-21	08-Nov-21	2	168	0%														
I1020	DRAINAGE INSTALLATION	09-Nov-21	22-Nov-21	10	168	0%														
I1030	LOW PRESSURE INSTALLATION AND TESTING	23-Nov-21	29-Nov-21	5	197	0%														
I1040	WATER SERVICES CONNECTIONS	23-Nov-21	26-Nov-21	4	198	0%														
I1050	ELECTRICAL CONDUIT INSTALLATION	23-Nov-21	29-Nov-21	5	168	0%														
I1060	ROAD SUBGRADE INSTALLATION	30-Nov-21	06-Dec-21	5	197	0%														
I1070	CONCRETE CURBING AND DRIVEWAYS	07-Dec-21	16-Dec-21	8	197	0%														
I1080	ROAD LIMEROCK INSTALLATION/GRADING	17-Dec-21	28-Dec-21	8	197	0%														
I1090	PAVING 1ST LIFT OF ASPHALT	29-Dec-21	30-Dec-21	2	197	0%														
I1100	REMOVAL OF TEMPORARY ROAD	31-Dec-21	03-Jan-22	2	197	0%														
I1110	SOD INSTALLATION	04-Jan-22	06-Jan-22	3	197	0%														
ICV 2.09	HOUSE # 41 THRU # 38, STA: 509+00 -> 504+00	30-Nov-21	06-Jan-22	28	197	0%														06-Jan-22, ICV
J1000	ROAD MILLING/DEMO	30-Nov-21	01-Dec-21	2	168	0%														
J1010	TEMPORARY ROAD INSTALLATION	02-Dec-21	02-Dec-21	1	168	0%														
J1020	DRAINAGE INSTALLATION	03-Dec-21	10-Dec-21	6	168	0%														
J1030	LOW PRESSURE INSTALLATION AND TESTING	13-Dec-21	15-Dec-21	3	197	0%														
J1040	WATER SERVICES CONNECTIONS	13-Dec-21	14-Dec-21	2	198	0%														
J1050	ELECTRICAL CONDUIT INSTALLATION	13-Dec-21	15-Dec-21	3	168	0%														
J1060	ROAD SUBGRADE INSTALLATION	16-Dec-21	20-Dec-21	3	197	0%														
J1070	CONCRETE CURBING AND DRIVEWAYS	21-Dec-21	27-Dec-21	5	197	0%														
J1080	ROAD LIMEROCK INSTALLATION/GRADING	28-Dec-21	31-Dec-21	4	197	0%														
J1090	PAVING 1ST LIFT OF ASPHALT	03-Jan-22	03-Jan-22	1	197	0%														
J1100	REMOVAL OF TEMPORARY ROAD	04-Jan-22	04-Jan-22	1	197	0%														
J1110	SOD INSTALLATION	05-Jan-22	06-Jan-22	2	197	0%														

Run Date February 3, 2021 as of April 1, 2021

Final Completion Date April 28, 2022

Project Completion: 0%

Start Date April 1, 2021

Construction Start Date April 30, 2021

4 of 6

INDIAN CREEK VILLAGE ROADWAY REDEVELOPMENT PROJECT

ENGINEER: STANTEC, CORAL GABLES FL

GIANNETTI CONTRACTING PROJECT No F-XXX

Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

INDIAN CREEK VILLAGE

Construction Schedule

04-Feb-21 08:11

Activity ID	Activity Name	Planned Start	Planned Finish	Original Duration	Total Float	Activity % Complete	2021				2022									
							Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4				
M1050	FINAL STRIPING	14-Apr-22	27-Apr-22	10	168	0%														
M1060	PROJECT CLOSEOUT	28-Apr-22	28-Apr-22	1	168	0%														

Run Date February 3, 2021 as of April 1, 2021
 Final Completion Date April 28, 2022
 Project Completion: 0%
 Start Date April 1, 2021
 Construction Start Date April 30, 2021

6 of 6
 INDIAN CREEK VILLAGE ROADWAY REDEVELOPMENT PROJECT
 ENGINEER: STANTEC, CORAL GABLES FL
 GIANNETTI CONTRACTING PROJECT No F-XXX

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- Summary

SECTION 00300

PROPOSAL
ROADWAY REDEVELOPMENT PROJECT
INDIAN CREEK VILLAGE, FLORIDA

Village Clerk's Office
Indian Creek Village
9080 Bay Drive
Indian Creek, Florida 33154

The undersigned, as Bidder, hereby declares that the only person or persons interested in the Proposal, as principal or principals, is or are named herein and that no other person than herein mentioned has any interest in the Proposal of the Contract to which the work pertains; that this Proposal is made without connection or arrangement with any other person, company, or parties making a bid or proposal and that the Proposal is in all respects fair and made in good faith without collusion or fraud.

The Bidder further declares that he has examined the site of the work and that from personal knowledge and experience, or that he has made sufficient observations of the conditions of the proposed Project Site to satisfy himself that such site is a correct and suitable one for this work and he assumes full responsibility therefore, that he has examined the Drawings and Specifications for the work and from his own experience or from professional advice that the Drawings, including bid item quantities, and Specifications are sufficient for the work to be done and he has examined the other Contractual Documents relating thereto, including the Notice of Bid Invitation, Instructions to Bidders, Proposal, Contract, General Conditions, Supplementary Conditions, Special Conditions, Technical Specifications, Drawings and has read all addenda prior to the receipt of bids, and that he has satisfied himself fully, relative to all matters and conditions with respect to the work to which this Proposal pertains.

The Bidder proposes and agrees, if this Proposal is accepted, to contract with the Indian Creek Village (Owner), in the form of contract specified, to furnish all necessary materials, all equipment, all necessary machinery, tools, apparatus, means of transportation, and labor necessary to complete the work specified in the Proposal and the Contract, and called for by the Drawings and Specifications and in the manner specified.

The Bidder further proposes and agrees to comply in all respects with the time limits for commencement and completion of the work as stated in the Contract Form.

The Bidder further agrees that the deductions for liquidated damages, as stated in the Contract Form, constitute fixed, agreed, and liquidated damages to reimburse the Owner for additional costs to the Owner resulting from the work not being completed within the time limit stated in the Contract Form.

Payment Bonds each in the amount of one-hundred percent of the Contract price, within ten (10) consecutive calendar days after written notice being given by the Owner of the award of the Contract, and the undersigned agrees that in case of failure on his part to execute the said Contract and Performance and Payment Bonds within the ten (10) consecutive calendar days after the award of the Contract, the cashier's check or Bid Bond accompanying his bid and the money payable thereon shall be paid to the Owner as liquidation of damages sustained by the Owner; otherwise, the check accompanying the Proposal shall be returned to the undersigned after the Contract is

signed and the Performance and Payment Bonds are filed.

The undersigned agrees to accept in full compensation therefore the total of the lump sum prices for the items named in the following schedule, based on the plan quantities contained within this bid form. Furthermore, the undersigned has checked these quantities and agrees that bid quantities are correct and adequate to complete the job in its entirety, as described in the contract document.

Bidders Certificate of Competency No. CGC1519762
CUC1225383
Bidders Occupational License No. CFC1429772

Acknowledgment is hereby made of the following Addenda received since issuance of the Project Manual:

Addendum No. 1 Dated: 1/20/2021 Addendum No. _____ Dated: _____
Addendum No. _____ Dated: _____ Addendum No. _____ Dated: _____
Addendum No. _____ Dated: _____ Addendum No. _____ Dated: _____

Attached hereto is a cashier's check on the _____
_____ Bank of _____
_____ of **Bid Bond** for the sum of Seven Hundred Seven
Thousand Nine Hundred dollars and eighty-five cents Dollars
(\$ 707,900.85), made payable to the Indian Creek Village, Florida.

Giannetti Contracting Corporation L.S.
(Name of Bidder) (Affix Seal)

 L.S.
Signature of Officer

Richard Gibbs III, President & Treasurer L.S.
(Title of Officer)

Address: 1801 NW 18th Street

City: Pompano Beach State: Florida

The full names and residences of persons and firms interested in the foregoing bid, as principals, are as follows:

Richard Gibbs III 1801 NW 18th St., Pompano Beach, Fl. 33069

Nicholas J. Apostol 1801 NW 18th St., Pompano Beach, Fl. 33069

Name of the executive who will give personal attention to the work:

Richard Gibbs III, President & Treasurer

LIST OF MAJOR SUB-CONTRACTORS

Bidders are required to list with the Proposal, on this sheet all major sub-contractors included for the prosecution of the work. Failure to complete the list may be cause for declaring the Proposal irregular.

The successful bidder shall employ the sub-contractors listed hereunder for the class of work indicated, which list shall not be modified in any way without the written consent of the Indian Creek Village.

The Bidder expressly agrees that:

1. If awarded a contract as a result of this proposal, the major sub-contractors used in the prosecution of the work will be those listed below.
2. The Bidder represents that the sub-contractors listed below are financially responsible and are qualified to do the work required.

CATEGORY OR CLASS	NAME OF SUB-CONTRACTOR	ADDRESS OF WORK
Electrical	South Florida Electrical Consulting, Inc.	4234 SW 75th Ave., Miami, Fl. 33155
Paving	Municipal Contractors	8958 Cypress Grove Lane, West Palm Beach, Fl. 33411
Concrete	Homestead Concrete and Drainage, Inc.	221 SW 4th Ave., Homestead, Fl. 33030
Landscape	Arazoza Bros., Corp.	PO Box 924890, Homestead, Fl. 33092
Rubber Trail	Rubaroc USA LLC	181 Edgemoor Rd., Wilmington, DE 19809

ROADWAY REDEVELOPMENT PROJECT
Indian Creek Village, Florida

BID FORM – ADDENDUM #1 CHANGES HIGHLIGHTED IN YELLOW


Bid unit prices stated in this proposal include all costs and expenses for labor, equipment, materials, contractor's overhead and profit. Unit prices for the various work items are intended to establish a total price for completing the project in its entirety. The Contractor shall include in the Bid price any work item and materials for which a separate pay item has not been included in the Bid Form. All work and incidental costs shall be included for payment under the several scheduled items of the overall contract, and no separate payment will be made therefore.

BASE BID

ITEM	DESCRIPTION	QUANTITY	UNIT	UNIT PRICE	AMOUNT
<u>Island - Roadway (RD) Items</u>					
RD-1	Standard clearing & grubbing, including tree removals	1	L.S.	\$ <u>52,189</u>	\$ <u>52,189</u>
RD-2	Demolition, removal & disposal of existing asphalt pavement and base	29,470	S.Y.	\$ <u>15</u>	\$ <u>442,050</u>
RD-3	Demolition, removal & disposal of existing concrete curb and gutter, curb, or valley gutter	10,502	L.F.	\$ <u>12</u>	\$ <u>126,024</u>
RD-4	Adjustment of existing utility and drainage manhole covers, valves, inlets, etc. to finish grade	1	L.S.	\$ <u>30,747</u>	\$ <u>30,747</u>
RD-5	12" Stabilized subgrade (shall include testing lab for tests every 100', each lane)	23,306	S.Y.	\$ <u>3</u>	\$ <u>69,918</u>
RD-6	10" Limerock base including BX1100 Geogrid (shall include testing lab for tests every 100', each lane)	23,306	S.Y.	\$ <u>33</u>	\$ <u>769,098</u>
RD-7	1" Thick Asphaltic Concrete Friction Course Type FC-9.5	23,306	S.Y.	\$ <u>11</u>	\$ <u>256,366</u>
RD-8	2" Thick Asphaltic Concrete Structural Course Type SP-9.5	23,306	S.Y.	\$ <u>21</u>	\$ <u>489,426</u>
RD-9	Embankment/fill material	1	L.S.	\$ <u>32,591</u>	\$ <u>32,591</u>
RD-10	Harmonization and restoration of existing landscaping and driveways behind new trail and curbs	1	L.S.	\$ <u>180,250</u>	\$ <u>180,250</u>

Giannetti Contracting Corporation

Name of Bidder


Signature of Bidder

00300-5

215615771


Roadway Redevelopment Project – Indian Creek Village, Florida

ITEM	DESCRIPTION	QUANTITY	UNIT	UNIT PRICE	AMOUNT
RD-11	Relocation/rotation of existing mailboxes (all mailboxes currently facing the street will need to be moved to face the existing driveway at location determined in the field)	30	EA.	\$ <u>2,732</u>	\$ <u>81,960</u>
RD-12	Paved concrete crosswalk including 12" wide concrete bands and concrete base	275	S.F.	\$ <u>26</u>	\$ <u>7,150</u>
RD-13	Concrete driveway approach (between gutter and new trail) colored with Scofield Chromix G and L Admixtures (or approved equal)	17,885	S.F.	\$ <u>9</u>	\$ <u>160,965</u>
RD-14	Provide all pavement markings and rpms as indicated on plans. Includes removal of all existing signage.	1	L.S.	\$ <u>6,743</u>	\$ <u>6,743</u>
RD-15	New signage including sign, decorative frame, pole, base cover and concrete footing	22	EA.	\$ <u>2,300</u>	\$ <u>50,600</u>
RD-16	Fully Engineering Segmental Retaining wall along view lot (including signed and sealed calculations)	700	L.F.	\$ <u>200</u>	\$ <u>140,000</u>
RD-17	Temporary road construction for vehicular traffic through work zone	1	AL.	\$300,000	\$300,000
Sub-total Island-RD Items					\$ <u>3,196,077</u>

Island - Electrical (E) Items

E-1	Furnish and install new complete street/sidewalk light pole including fixture, base, ballast, wiring, bulb, etc.	100	EA.	\$ <u>5,900</u>	\$ <u>590,000</u>
E-2	Furnish and install electrical conduit, including fittings, wiring, grounding, pullboxes, restoration, etc.	10,005	L.F..	\$ <u>47</u>	\$ <u>470,235</u>
E-3	Furnish and install electrical service points including all panels, disconnects, wiring, frame, concrete slabs and foundations, coordination and service run to FPL connection point, etc.	5	EA.	\$ <u>24,295</u>	\$ <u>121,475</u>
Sub-total Island - E items					\$ <u>1,181,710</u>

Giannetti Contracting Corporation
 Name of Bidder


 Signature of Bidder

Roadway Redevelopment Project – Indian Creek Village, Florida

ITEM	DESCRIPTION	QUANTITY	UNIT	UNIT PRICE	AMOUNT
Island - Stormwater (SW) Items					
SW-1	Type "A" concrete curb and gutter, colored with Scofield Chromix G and L Admixtures (or approved equal)	9,409	L.F.	\$ <u>24</u>	\$ <u>225,816</u>
SW-2	12" wide concrete gutter, colored with Scofield Chromix G and L Admixtures (or approved equal)	8,922	L.F.	\$ <u>22</u>	\$ <u>196,284</u>
SW-3	16" wide concrete gutter, colored with Scofield Chromix G and L Admixtures (or approved equal)	570	L.F.	\$ <u>27</u>	\$ <u>15,390</u>
SW-4	Type "D" concrete curb, colored with Scofield Chromix G and L Admixtures (or approved equal)	1,309	L.F.	\$ <u>21</u>	\$ <u>27,489</u>
SW-5	5' wide Trail (Rubberway Rubberrock Evolution Multi 6000 Flexible Pervious Pavement or approved equal) including all edging and subsurface material as shown in detail. Shall include testing lab for compaction tests every 100'.	43,601	S.F.	\$ <u>16</u>	\$ <u>697,616</u>
SW-6	Type 'P' manhole or Catch Basin, including structure, inlet, frame, cover, and baffle where required.	95	E.A.	\$ <u>8,000</u>	\$ <u>760,000</u>
SW-7	Type 9 Catch Basin, including structure, inlet, frame, cover, and baffle where required.	0	E.A.	\$ <u>9,500</u>	\$ <u>0.00</u>
SW-8	Type 10 Catch Basin, including structure, inlet, frame, cover, and baffle where required.	0	E.A.	\$ <u>9,500</u>	\$ <u>0.00</u>
SW-9	Two or three chamber Outfall control structure including weir wall(s), frame, cover, etc.	12	E.A.	\$ <u>22,000</u>	\$ <u>264,000</u>
SW-10	12" Nyloplast ADS yard drain or approved equal	5	E.A.	\$ <u>3,000</u>	\$ <u>15,000</u>
SW-11	18" diameter HDPE solid pipe	673	L.F.	\$ <u>120</u>	\$ <u>80,760</u>
SW-12	24" diameter HDPE solid pipe	285	L.F.	\$ <u>135</u>	\$ <u>38,475</u>
SW-13	30" diameter HDPE solid pipe	220	L.F.	\$ <u>140</u>	\$ <u>30,800</u>
SW-14	30" diameter, 4-ft wide exfiltration trench	7,850	L.F.	\$ <u>155</u>	\$ <u>1,216,750</u>
SW-15	Manatee Grate per the latest edition of FDOT standard index	12	E.A.	\$ <u>1,500</u>	\$ <u>18,000</u>

Giannetti Contracting Corporation

Name of Bidder



Signature of Bidder

Roadway Redevelopment Project – Indian Creek Village, Florida

ITEM	DESCRIPTION	QUANTITY	UNIT	UNIT PRICE	AMOUNT
SW-16	8" Inline check valve	1	E.A.	\$ <u>3,016</u>	\$ <u>3,016</u>
SW-17	10" Inline check valve	2	E.A.	\$ <u>3,753</u>	\$ <u>7,506</u>
SW-18	12" Inline check valve	3	E.A.	\$ <u>4,757</u>	\$ <u>14,271</u>
SW-19	18" Inline check valve	2	E.A.	\$ <u>9,540</u>	\$ <u>19,080</u>
SW-20	24" Inline check valve	2	E.A.	\$ <u>12,756</u>	\$ <u>25,512</u>
Sub-total Island – SW Items					\$ <u>3,655,765</u>


Island - Landscaping/Irrigation (LI) Items

LI-1	Landscaping - Complete	1	L.S.	\$ <u>459,098</u>	\$ <u>459,098</u>
LI-2	Zoysia Sod from front of trail to back of curb including grading and soil preparation	46,640	S.F.	\$ <u>1.70</u>	\$ <u>79,288</u>
LI-3	Protection of existing trees and landscaping	1	L.S.	\$ <u>49,159</u>	\$ <u>49,159</u>
LI-4	Irrigation System Complete including connections to service points and restoration of existing - Allowance	1	AL.	\$225,000	\$225,000
Sub-total Island - LI Items					\$ <u>812,545</u>

Island – Water & Sewer (WS) Items

WS-1	Furnish and Install Duplex Grinder Pump Station Package (Including Electrical and Fittings) WH-472-92 See Details.	42	EA.	\$ <u>21,754</u>	\$ <u>913,668</u>
WS-2	Furnish and Install Quadplex Grinder Pump Station Package (Including Electrical and Fittings)	1	EA.	\$ <u>41,628</u>	\$ <u>41,628</u>
WS-3	Furnish and Install SDR11 HDPE forcemain (Including all fittings & valves for all pipe sizes and termination point)	10,735	L.F.	\$ <u>34</u>	\$ <u>364,990</u>
WS-4	Relocation of existing fire hydrants including those required to move to construct temporary pavement within work zone	19	EA.	\$ <u>2,500</u>	\$ <u>47,500</u>
WS-5	Replacement of existing 2" water service line and meter box (meter to be provided by the Village, installed by contractor)	71	EA.	\$ <u>4,200</u>	\$ <u>298,200</u>

Giannetti Contracting Corporation
Name of Bidder


Signature of Bidder

Roadway Redevelopment Project – Indian Creek Village, Florida

ITEM	DESCRIPTION	QUANTITY	UNIT	UNIT PRICE	AMOUNT
WS-6	New 2" Irrigation meter, including service line, meter box, backflow prevention, etc.	3	EA.	\$ <u>4,700</u>	\$ <u>14,100</u>
Sub-total Island - WS Items					\$ <u>1,680,086</u>
<u>General (G) Items</u>					
G-1	Mobilization	1	L.S.	\$ <u>125,000</u>	\$ <u>125,000</u>
G-2	Stormwater pollution prevention measures including erosion, sedimentation and dust control and turbidity barriers (to be divided equally for each month of construction).	1	L.S.	\$ <u>85,000</u>	\$ <u>85,000</u>
G-3	Maintenance of traffic, including traffic control, pedestrian and vehicular access, signs, barricades, flaggers, and variable message boards (to be divided equally for each month of construction).	1	L.S.	\$ <u>45,000</u>	\$ <u>45,000</u>
G-4	Performance & Payment Bond	1	L.S.	\$ <u>88,804</u>	\$ <u>88,804</u>
G-5	General Conditions including bonds, insurance, management, supervision, etc. (to be divided equally for each month of construction)	1	L.S.	\$ <u>2,214,000</u>	\$ <u>2,214,000</u>
G-6	Compliance with Safety Act	1	L.S.	\$ <u>59,536</u>	\$ <u>59,536</u>
G-7	Advance exploration of existing utilities	1	L.S.	\$ <u>61,494</u>	\$ <u>61,494</u>
G-8	Record As-built drawings	1	L.S.	\$ <u>153,000</u>	\$ <u>153,000</u>
G-9	Contingency – Allowance	1	AL.	\$750,000	\$750,000
G-10	Police – Allowance	1	AL.	\$50,000	\$50,000
Sub-total G Items					\$ <u>3,631,834</u>

GRAND TOTAL (BASE BID) IN FIGURES (LUMP SUM): \$ 14,158,017.00

GRAND TOTAL (BASE BID) WRITTEN: Fourteen Million One Hundred Fifty-Eight Thousand Seventeen Dollars and Zero Cents

BIDDER: Giannetti Contracting Corporation


By: 

Title: Richard Gibbs III, President & Treasurer

Telephone: 954-972-8104

Fax: 954-972-8108

Giannetti Contracting Corporation
Name of Bidder


Signature of Bidder

Construction of Roadway Redevelopment Project – Indian Creek Village, Florida

ITEM	DESCRIPTION	QUANTITY	UNIT	UNIT PRICE	AMOUNT
-------------	--------------------	-----------------	-------------	-------------------	---------------

By signing below, the bidder confirms their ability to meet the overall project schedule which requires all work to be substantially complete within five-hundred and forty (540) calendar days from the date authorized to proceed.

BIDDER: Giannetti Contracting Corporation


By: 

Title: Richard Gibbs III, President & Treasurer

Telephone: 954-972-8104

Fax: 954-972-8108

Giannetti Contracting Corporation
Name of Bidder


Signature of Bidder

INDIAN CREEK VILLAGE, FLORIDA



NOTICE TO BIDDERS

All bidders are notified that the Village intends to implement a "sales tax savings" accounting procedure to avoid the collection of State and Local sales tax on the project.

All bidders are to **INCLUDE** all applicable sales tax in their bid.

The successful, awarded contractor will cooperate with the Village accounting department to implement to implement a purchase order system which will allow the Village to pay directly for all materials purchased for the direct execution and incorporation into the project. The overall contract amount will subsequently be reduced by formal change order for all material directly paid for and sales tax saved with the implementation of this procedure.


Acknowledgment:

Giannetti Contracting Corporation

Contractor

Attest: 

Attest: _____

By: 
Richard Gibbs III, President & Treasurer
January 20, 2021

Date

NON-COLLUSION AFFIDAVIT

STATE OF Florida
COUNTY OF Broward

Richard Gibbs III ("Affiant"), being first duly sworn, deposes and says that:


- 1. Affiant is President, Treasurer, & Partner of Giannetti Contracting Corporation, (the "Bidder") and has submitted the attached Bid;
- 2. Affiant has personal knowledge of the matters set forth herein and is competent to testify;
- 3. Affiant is fully informed respecting the preparation and contents of the attached Bid and all pertinent circumstances respecting the Bid;
- 4. The Bid is genuine and is not a collusive or sham Bid;
- 5. Neither the Bidder nor any of its officers, partners, owners, agents, representatives, employees, or parties in interest, including Affiant, has in any way colluded, conspired, connived, or agreed, directly or indirectly with any other Bidder, firm, or person to submit a collusive or sham Bid, or has in any manner, directly or indirectly, sought by agreement or collusion or communication or conference with any other Bidder, firm, or person to fix the price or prices in the attached Bid or of any other Bidder, or to fix any overhead, profit, or cost element of the Bid price or the Bid price of any other Bidder, or to secure through any collusion, conspiracy, connivance or unlawful agreement any advantage against Indian Creek Village or any person interested in the proposed Contract.

By: [Signature]



Title: Richard Gibbs III, President & Treasurer

Subscribed and sworn before me this 20 day of January, 2021, by Richard Gibbs III, who is personally known to me or has produced as identification.



[Signature]

Notary Public

Marcia West

Print Name

My commission expires:

**CERTIFICATION REGARDING
DEBARMENT, SUSPENSION, INELIGIBILITY AND VOLUNTARY EXCLUSION
LOWER TIER COVERED TRANSACTIONS**

This certification is required by the regulations implementing Executive Order 12549, Debarment and Suspension, 45 CFR 1183.35, Participants' responsibilities. The regulations were published as Part VII of the May 26, 1988 Federal Register (pages 19160-19211). Copies of the regulations may be obtained by contacting the person to which this proposal is submitted.

(BEFORE COMPLETING CERTIFICATION, READ INSTRUCTIONS ON REVERSE)

(1) The prospective lower tier participant certifies, by submission of this proposal, that neither it nor its principals are presently debarred, suspended, proposed for debarment, declared ineligible, or voluntarily excluded from participation in this transaction by any federal department or agency.

(2) Where the prospective lower tier participant is unable to certify to any of the statements in this certification, such prospective participant shall attach an explanation to this proposal.

Giannetti Contracting Corporation

Organization Name

Richard Gibbs III, President & Treasurer

Name and Title of Authorized Representative

Signature

January 20, 2021

Date

INSTRUCTIONS FOR CERTIFICATION

1. By signing and submitting this proposal, the prospective lower tier participant is providing the certification set out below.
2. The certification in this clause is a material representation of fact upon which reliance was placed when this transaction was entered into. If it is later determined that the prospective lower tier participant knowingly rendered an erroneous certification, in addition to other remedies available to the federal government, the department or agency with which this transaction originated may pursue available remedies, including suspension and/or debarment.
3. The prospective lower tier participant shall provide immediate written notice to the person to which this proposal is submitted if at any time the prospective lower tier participant learns that its certification was erroneous when submitted or has become erroneous by reason of changed circumstances.
4. The terms “covered transaction,” “debarred,” “suspended,” “ineligible,” “lower tier covered transaction,” “participant,” “person,” “primary covered transaction,” “principal,” “proposal,” and “voluntarily excluded,” as used in this clause, have the meanings set out in the Definitions and Coverage sections of rules implementing Executive Order 12549. You may contact the person to which this proposal is submitted for assistance in obtaining a copy of those regulations.
5. The prospective lower tier participant agrees by submitting this proposal that, should the proposed covered transaction be entered into, it shall not knowingly enter into any lower tier covered transaction with a person who is debarred, suspended, declared ineligible, or voluntarily excluded from participation in this covered transaction, unless authorized by the department or agency with which this transaction originated.
6. The prospective lower tier participant further agrees by submitting this proposal that it will include the clause titled “Certification Regarding Debarment, Suspension, Ineligibility, and Voluntary Exclusion-Lower Tier Covered Transactions,” without modification, in all lower tier covered transactions and in all solicitations for lower tier covered transactions.
7. A participant in a covered transaction may rely upon a certification of a prospective participant in a lower tier covered transaction that it is not debarred, suspended, ineligible, or voluntarily excluded from the covered transaction, unless it knows that the certification is erroneous. A participant may decide the method and frequency by which it determines the eligibility of its principals. Each participant may, but is not required to, check the Nonprocurement List (Telephone Number).
8. Nothing contained in the foregoing shall be construed to require establishment of a system of records in order to render in good faith the certification required by this clause. The knowledge and information of a participant is not required to exceed that which is normally possessed by a prudent person in the ordinary course of business dealings.
9. Except for transactions authorized under paragraph 5 of these instructions, if a participant in a covered transaction knowingly enters into a lower tier covered transaction with a person who is suspended, debarred, ineligible, or voluntary excluded from participation in this transaction, in addition to other remedies available to the federal government, the department or agency with which this transaction originated may pursue available remedies, including suspension and/or debarment.

SECTION 00350

CONTRACTOR'S QUESTIONNAIRE

Submitted to: The Mayor and Village Council of the Indian Creek Village, Florida:

By Giannetti Contracting Corporation

Principal Office 1801 NW 18th St., Pompano Beach, Fl. 33069

How many years has your organization been in business as a General Contractor under your present business name? 35 years

Does your organization have current occupational licenses entitling it to do the work contemplated in this Contract? Yes

State of Florida Occupational License (State type and number):
CGC1519762 CUC1225383 CFC1429772

Federal I.D. No: 38-2477625

Dade County Certificate of Competency (State type and number):
N/A

Indian Creek Village Occupational License (State type and number):
N/A

Please include copies of above licenses and certifications with proposal.

How many years experience in similar work has your organization had?

- (A) As a General Contractor 35
- (B) As a Sub-Contractor 35
- (C) What contracts has your organization completed? State below:

Contract Amount	Class of Work	When Completed	Name & Address of Owner
\$8,642,718.50	Neighborhood Infrastructure on Island	2019	City of Riviera Beach 600 W. Blue Heron Blvd., Riviera Beach, Fl.
\$13,689,489.38	WM & Drainage Replacement	2018	City of Hollywood, Florida 2600 Hollywood Blvd., Hollywood, Fl.
\$8,912,466.41	Neighborhood Infrastructure on Island	2018	Loxahatchee River District 2500 Jupiter Park Dr. , Jupiter, Fl

How many years has your organization, or your concrete curb and sidewalk sub-contractor had in the actual construction of municipal, decorative sidewalks and streetscapes?

35 years

<u>Name & tel. number of Owner</u>	<u>Project Name</u>	<u>Date completed</u>
City of Riviera Beach, Florida Terrence Bailey, PE 561-845-4080	Yacht Harbor Manor Roadway Project	November 2019
City of Hollywood, Florida Clece Aurelus, PE 954-967-4455	Water Main Replacement Program - Hollywood Blvd. to Sheridan St., Federal Hwy. to Intracostal Waterway	August 2018
Loxahatchee River District Kris Dean, PE 561-747-5700	Jupiter Inlet Colony Neighborhood Rehabilitation Project	April 2018

Have you ever failed to complete any work awarded to you? No

If so, where and why? _____

Has any officer or partner of your organization ever failed to complete a contract handled in his own name? No

If so, state name of individual, name of owner, and reason thereof:

In what other lines of business are you financially interested or engaged?

None

Give references as to experience, ability and financial standing.

See project references for construction experience.

TCF National Bank Banking 248-244-6897
Scott D. Dorn, Vice-President, TCF Middle Market sdorn@tcfbank.com
Guy Hurley, LLC Surety & Insurance Agent
Michael Lechner, Vice-President mlechner@ghbh.com 248-519-1400

What equipment do you own that is available for the proposed work and where is it located?

See attached equipment list

All of our equipment is located in South Florida
and our lowboy tractors are constantly moving equipment.


Financial Statement: See attached

What Bank or Banks have you arranged to do business with during the course of the Contract should it be awarded to you?


TCF National Bank

I hereby certify that the above answers are true and correct.

Name of Bidder: Giannetti Contracting Corporation

Signature of Officer: 

Title of Officer: Richard Gibbs III, President & Treasurer



END OF SECTION

SECTION 00410

BID BOND

STATE OF FLORIDA)
SS
COUNTY OF)

KNOW ALL MEN BY THESE PRESENTS, that Giannetti Contracting Corporation
as Principal, and
Arch Insurance Company, as Surety,
a Corporation chartered and existing under the laws of the State of Missouri, with its
principal offices in the City of Jersey City, NJ, and authorized to do business in the State of
Florida are held and firmly bound unto the Owner, Indian Creek Village, Florida in
the penal sum of Five Percent of the Amount of Bid
Dollars (\$ 5%) lawful money of
the United States, for the payment of which sum will and truly to be made, we bind ourselves, our
heirs, executors, administrators, and successors, jointly and severally, firmly by these presents.

THE CONDITION OF THIS OBLIGATION IS SUCH, that whereas the Principal has
submitted the accompanying bid, dated February 4, 2021, for:


ROADWAY REDEVELOPMENT PROJECT
Indian Creek Village, Florida

NOW, THEREFORE:



- A. If the principal shall not withdraw said bid within sixty (60) days after date of opening
of the same, and shall within ten (10) days after the prescribed forms are presented
to him for signature, enter into a written contract with the Owner in accordance with
the bid as accepted, and give bonds with good and sufficient surety or sureties, as
may be required, for the faithful performance and proper fulfillment of such contract,
then the above obligations shall be void and of no effect, otherwise to remain in full
force and effect.
B. In the event of the withdrawal of said bid within the period specified, or the failure to
enter into such contract and give such bonds within the time specified, if the
principal shall pay the Owner the difference between the amount specified in said
bid and the amount for which the Owner may procure the required work and
supplies, if the latter amount be in excess of the former, then the above obligations
shall be void and of no effect, otherwise to remain in full force and effect.



IN WITNESS WHEREOF, the above bounded parties have executed this instrument under their several seals, this 4th day of February, A.D., 20 21, the name and corporate seal of each corporate party being hereto affixed and these presents duly signed by its undersigned representative, pursuant to authority of its governing body.

WITNESSES: (If Sole Ownership or Partnership, two (2) witnesses required).
(If Corporation, Secretary Only will attest and affix seal).


WITNESSES:


PRINCIPAL:

Giannetti Contracting Corporation
Name of Firm

Signature of Authorized (Affix Seal) 
Richard Gibbs, President
Title
1801 NW 18th Street
Business Address
Pompano Beach, FL 33069
City, State & Zip Code

WITNESSES:

Jessica Nightenhelser

Christina Riley

SURETY:

Arch Insurance Company
Corporate Surety

Attorney-in-Fact (Affix Seal) Holly Nichols
210 Hudson Street, Suite 300
Business Address
Jersey City, NJ 07311-1107
City, State & Zip Code
Guy Hurley, LLC
Name of Local Insurance Agency

THIS POWER OF ATTORNEY IS NOT VALID UNLESS IT IS PRINTED ON BLUE BACKGROUND.

This Power of Attorney limits the acts of those named herein, and they have no authority to bind the Company except in the manner and to the extent herein stated. Not valid for Note, Loan, Letter of Credit, Currency Rate, Interest Rate or Residential Value Guarantees.

POWER OF ATTORNEY

Know All Persons By These Presents:

That the Arch Insurance Company, a corporation organized and existing under the laws of the State of Missouri, having its principal administrative office in Jersey City, New Jersey (hereinafter referred to as the "Company") does hereby appoint:

Holly Nichols, Mark T. Madden, Michael D. Lechner, Nicholas Ashburn, Richard McGregor and Robert D. Heuer of Troy, MI (EACH)

its true and lawful Attorney(s)in-Fact, to make, execute, seal, and deliver from the date of issuance of this power for and on its behalf as surety, and as its act and deed:

Any and all bonds, undertakings, recognizances and other surety obligations, in the penal sum not exceeding Ninety Million Dollars (\$90,000,000.00).

This authority does not permit the same obligation to be split into two or more bonds in order to bring each such bond within the dollar limit of authority as set forth herein.

The execution of such bonds, undertakings, recognizances and other surety obligations in pursuance of these presents shall be as binding upon the said Company as fully and amply to all intents and purposes, as if the same had been duly executed and acknowledged by its regularly elected officers at its principal administrative office in Jersey City, New Jersey.

This Power of Attorney is executed by authority of resolutions adopted by unanimous consent of the Board of Directors of the Company on September 15, 2011, true and accurate copies of which are hereinafter set forth and are hereby certified to by the undersigned Secretary as being in full force and effect:

"VOTED, That the Chairman of the Board, the President, or the Executive Vice President, or any Senior Vice President, of the Surety Business Division, or their appointees designated in writing and filed with the Secretary, or the Secretary shall have the power and authority to appoint agents and attorneys-in-fact, and to authorize them subject to the limitations set forth in their respective powers of attorney, to execute on behalf of the Company, and attach the seal of the Company thereto, bonds, undertakings, recognizances and other surety obligations obligatory in the nature thereof, and any such officers of the Company may appoint agents for acceptance of process."

This Power of Attorney is signed, sealed and certified by facsimile under and by authority of the following resolution adopted by the unanimous consent of the Board of Directors of the Company on September 15, 2011:

VOTED, That the signature of the Chairman of the Board, the President, or the Executive Vice President, or any Senior Vice President, of the Surety Business Division, or their appointees designated in writing and filed with the Secretary, and the signature of the Secretary, the seal of the Company, and certifications by the Secretary, may be affixed by facsimile on any power of attorney or bond executed pursuant to the resolution adopted by the Board of Directors on September 15, 2011, and any such power so executed, sealed and certified with respect to any bond or undertaking to which it is attached, shall continue to be valid and binding upon the Company.

SECTION 00650

CERTIFICATE OF INSURANCE

THIS IS TO CERTIFY THAT THE Continental Casualty Company
(Insurance Company)
Address 1 Towne Sq Ste 1075 Southfield, MI 48076
of _____

has issued policies of insurance, as described below and identified by a policy number, to the insured named below; and to certify that such policies are in full force and effect at this time. It is agreed that none of these policies will be canceled or changed so as to affect the interest(s) of the Indian Creek Village (hereinafter sometimes called the Owner) until thirty (30) days after written notice of such cancellation or change has been delivered to the Engineer; Sean Compel, Stantec, Inc.

Insured Giannetti Contracting Corporation
Address 1801 NW 18th Street Pompano Beach, FL 33069

Status of Insured: Corporation Partnership Individual

Location of Operations Insured _____

Description of Work:

ROADWAY REDEVELOPMENT PROJECT
Indian Creek Village, Florida

INSURANCE POLICIES IN FORCE:

<u>Forms of Coverage</u> <u>Date</u>	<u>Policy Number</u>	<u>Exp.</u>
*Workers Comp./Employers Liability	<u>6079348208</u>	<u>12/01/2021</u>
+Comprehensive Automobile Liability	<u>6079348192</u>	<u>12/01/2021</u>
oComprehensive General Liability	<u>6079348189</u>	<u>12/01/2021</u>
+Excess Liability	<u>6079348211</u>	<u>12/01/2021</u>
Other (Please specify type: _____)	_____	_____

POLICY INCLUDES COVERAGE FOR:

	YES	NO
1. Additional Insured: Owner & Engineer	<u> X </u>	_____
2. *Liability under the United States Longshoremen's and Harbor Workers' Compensation Act.	<u> X </u>	_____
3. +All owned, hired, or nonowned automotive equipment used in connection with work done for the Owner.	<u> X </u>	_____
4. oContractual Liability	<u> X </u>	_____
5. oDamage caused by explosion, collapse or structural injury, and damage to underground utilities.	<u> X </u>	_____
6. oProducts/Completed Operations	<u> X </u>	_____
7. oOwners and Contractors Protective Liability	<u> X </u>	_____
8. oPersonal Injury Liability	_____	_____
9. +Excess Liability applies excess of:	<u> X </u>	_____
(a) Employers Liability	_____	_____
(b) Comprehensive General Liability	<u> X </u>	_____
(c) Comprehensive Automobile Liability	<u> X </u>	_____

TYPES OF POLICY	FORMS OF COVERAGE	LIMITS OF LIABILITY
Workers' Compensation	Bodily Injury	\$ Statutory
Employers Liability	Bodily Injury	\$ <u>1,000,000</u> Each Accident
	Disease	\$ <u>1,000,000</u> Each Person
	Disease	\$ <u>1,000,000</u> Policy Limit
Comprehensive Auto Liability	Combined Single Limit B/IPD	\$ <u>1,000,000</u> Each Accident

Comprehensive General Liability	Bodily Injury	\$1,000,000 Each Occurrence \$2,000,000 Aggregate
	Property Damage	\$1,000,000 Each Occurrence \$2,000,000 Aggregate
OR		
	Combined Single Limit BI/PD Occurrence	\$ _____ Each \$ _____ Aggregate

Excess Liability	Combined Single Limit BI/PD	\$5,000,000 Aggregate
------------------	-----------------------------	-----------------------

Other


The Insurance Company hereby agrees to deliver, within ten (10) days, two (2) copies of the above policies to the Engineer when so requested.

NOTE: Entries on this certificate are limited to the Authorized Agent or Insurance Company Representative.

Date 1-21-21

Issued at Bohertoe Hills MI

Insurance Agent or Company
-Send original and one copy to:

(SEAL)

 Insurance Company
 Authorized Representative

ANNE BAUCK
 NOTARY PUBLIC - STATE OF MICHIGAN
 MACOMB COUNTY
 My Commission Expires July 1, 2025
 Acting in the County of Dakeland

Stantec Consulting Services Inc.
 901 Ponce De Leon Boulevard, Suite 900
 Coral Gables, Florida 33134
 Attention: Sean Compel, P.E., Principal in Charge

Send two (2) copies to:

Indian Creek Village
 9080 Bay Drive
 Indian Creek Village, Florida 33154
 Attention: Jennifer Medina, Village Manager

END OF SECTION

00650-3

215615771



CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)
1/20/2021

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

PRODUCER Guy Hurley, LLC 989 E. South Blvd. Suite 200 Rochester Hills MI 480307	CONTACT NAME: Denielle Killenberg
	PHONE (A/C, No, Ext): (248) 519-1400 FAX (A/C, No): (248) 519-1401
	E-MAIL ADDRESS: dkillenberg@ghbh.com
	INSURER(S) AFFORDING COVERAGE NAIC #
INSURED Giannetti Contracting Corporation Giannetti Contracting of Florida, Inc. 6340 Sims Drive Sterling Heights MI 48313	INSURER A: National Fire Ins of Hartford A XV 20478
	INSURER B: Continental Casualty Co A XV 20443
	INSURER C: Continental Insurance Co A XV 35289
	INSURER D:
	INSURER E:

COVERAGES **CERTIFICATE NUMBER:** 20-21 LSD/RNTD **REVISION NUMBER:**

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	ADDL INSR	SUBR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS				
A	GENERAL LIABILITY			6079348189	12/1/2020	12/1/2021	EACH OCCURRENCE	\$ 1,000,000			
	<input checked="" type="checkbox"/> COMMERCIAL GENERAL LIABILITY						DAMAGE TO RENTED PREMISES (Ea occurrence)	\$ 100,000			
	<input type="checkbox"/> CLAIMS-MADE <input checked="" type="checkbox"/> OCCUR						MED EXP (Any one person)	\$ 5,000			
	<input checked="" type="checkbox"/> XCU Coverage Included						PERSONAL & ADV INJURY	\$ 1,000,000			
	<input checked="" type="checkbox"/> Contractual Liability						GENERAL AGGREGATE	\$ 2,000,000			
	GEN'L AGGREGATE LIMIT APPLIES PER:									PRODUCTS - COMP/OP AGG	\$ 2,000,000
	<input type="checkbox"/> POLICY <input checked="" type="checkbox"/> PRO-JECT <input type="checkbox"/> LOC										\$
A	AUTOMOBILE LIABILITY			6079348192	12/1/2020	12/1/2021	COMBINED SINGLE LIMIT (Ea accident)	\$ 1,000,000			
	<input checked="" type="checkbox"/> ANY AUTO						BODILY INJURY (Per person)	\$			
	<input type="checkbox"/> ALL OWNED AUTOS	<input type="checkbox"/> SCHEDULED AUTOS					BODILY INJURY (Per accident)	\$			
	<input checked="" type="checkbox"/> HIRED AUTOS	<input checked="" type="checkbox"/> NON-OWNED AUTOS					PROPERTY DAMAGE (Per accident)	\$			
							Drive other car	\$			
C	<input checked="" type="checkbox"/> UMBRELLA LIAB		<input checked="" type="checkbox"/> OCCUR	6079348211	12/1/2020	12/1/2021	EACH OCCURRENCE	\$ 5,000,000			
	<input type="checkbox"/> EXCESS LIAB		<input type="checkbox"/> CLAIMS-MADE				AGGREGATE	\$ 5,000,000			
	<input type="checkbox"/> DED <input checked="" type="checkbox"/> RETENTION \$		0					\$			
A	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY			6079348208	12/1/2020	12/1/2021	<input checked="" type="checkbox"/> WC STATUTORY LIMITS	<input type="checkbox"/> OTHER			
	ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH)	<input type="checkbox"/> Y <input checked="" type="checkbox"/> N	N/A				E.L. EACH ACCIDENT	\$ 1,000,000			
	If yes, describe under DESCRIPTION OF OPERATIONS below						E.L. DISEASE - EA EMPLOYEE	\$ 1,000,000			
							E.L. DISEASE - POLICY LIMIT	\$ 1,000,000			
B	Inland Marine			6079848045	12/1/2020	12/1/2021	Leased/Rented Equipment	\$500,000			

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (Attach ACORD 101, Additional Remarks Schedule, if more space is required)

CERTIFICATE HOLDER **CANCELLATION**

Indian Creek Village 9080 Bay Drive Indian Creek Village, FL 33154	SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.
	AUTHORIZED REPRESENTATIVE R McGregor/KILLEN



CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)
1/20/2021

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

PRODUCER Guy Hurley, LLC 989 E. South Blvd. Suite 200 Rochester Hills MI 480307	CONTACT NAME: Denielle Killenberg PHONE (A/C, No, Ext): (248) 519-1400 FAX (A/C, No): (248) 519-1401 E-MAIL ADDRESS: dkillenberg@ghbh.com														
INSURED Giannetti Contracting Corporation Giannetti Contracting of Florida, Inc. 6340 Sims Drive Sterling Heights MI 48313	<table border="1" style="width: 100%; border-collapse: collapse;"> <tr> <th style="text-align: center;">INSURER(S) AFFORDING COVERAGE</th> <th style="text-align: center;">NAIC #</th> </tr> <tr> <td>INSURER A: National Fire Ins of Hartford A XV</td> <td style="text-align: center;">20478</td> </tr> <tr> <td>INSURER B: Continental Casualty Co A XV</td> <td style="text-align: center;">20443</td> </tr> <tr> <td>INSURER C: Continental Insurance Co A XV</td> <td style="text-align: center;">35289</td> </tr> <tr> <td>INSURER D:</td> <td></td> </tr> <tr> <td>INSURER E:</td> <td></td> </tr> <tr> <td>INSURER F:</td> <td></td> </tr> </table>	INSURER(S) AFFORDING COVERAGE	NAIC #	INSURER A: National Fire Ins of Hartford A XV	20478	INSURER B: Continental Casualty Co A XV	20443	INSURER C: Continental Insurance Co A XV	35289	INSURER D:		INSURER E:		INSURER F:	
INSURER(S) AFFORDING COVERAGE	NAIC #														
INSURER A: National Fire Ins of Hartford A XV	20478														
INSURER B: Continental Casualty Co A XV	20443														
INSURER C: Continental Insurance Co A XV	35289														
INSURER D:															
INSURER E:															
INSURER F:															

COVERAGES **CERTIFICATE NUMBER: 20-21 LSD/RNTD** **REVISION NUMBER:**

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	ADDL INSR	SUBR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS
A	GENERAL LIABILITY			6079348189	12/1/2020	12/1/2021	EACH OCCURRENCE \$ 1,000,000
	<input checked="" type="checkbox"/> COMMERCIAL GENERAL LIABILITY						DAMAGE TO RENTED PREMISES (Ea occurrence) \$ 100,000
	<input type="checkbox"/> CLAIMS-MADE <input checked="" type="checkbox"/> OCCUR						MED EXP (Any one person) \$ 5,000
	<input checked="" type="checkbox"/> XCU Coverage Included						PERSONAL & ADV INJURY \$ 1,000,000
	<input checked="" type="checkbox"/> Contractual Liability						GENERAL AGGREGATE \$ 2,000,000
GEN'L AGGREGATE LIMIT APPLIES PER:							PRODUCTS - COMP/OP AGG \$ 2,000,000
<input type="checkbox"/> POLICY <input checked="" type="checkbox"/> PRO-JECT <input type="checkbox"/> LOC							\$
A	AUTOMOBILE LIABILITY			6079348192	12/1/2020	12/1/2021	COMBINED SINGLE LIMIT (Ea accident) \$ 1,000,000
	<input checked="" type="checkbox"/> ANY AUTO						BODILY INJURY (Per person) \$
	<input type="checkbox"/> ALL OWNED AUTOS <input type="checkbox"/> SCHEDULED AUTOS						BODILY INJURY (Per accident) \$
	<input checked="" type="checkbox"/> HIRED AUTOS <input checked="" type="checkbox"/> NON-OWNED AUTOS						PROPERTY DAMAGE (Per accident) \$
Drive other car \$							
C	<input checked="" type="checkbox"/> UMBRELLA LIAB <input checked="" type="checkbox"/> OCCUR			6079348211	12/1/2020	12/1/2021	EACH OCCURRENCE \$ 5,000,000
	<input type="checkbox"/> EXCESS LIAB <input type="checkbox"/> CLAIMS-MADE						AGGREGATE \$ 5,000,000
	<input type="checkbox"/> DED <input checked="" type="checkbox"/> RETENTION \$ 0						\$
A	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY			6079348208	12/1/2020	12/1/2021	<input checked="" type="checkbox"/> WC STATUTORY LIMITS <input type="checkbox"/> OTHER
	ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH)	Y/N	N/A				E.L. EACH ACCIDENT \$ 1,000,000
	If yes, describe under DESCRIPTION OF OPERATIONS below						E.L. DISEASE - EA EMPLOYEE \$ 1,000,000
							E.L. DISEASE - POLICY LIMIT \$ 1,000,000
B	Inland Marine			6079848045	12/1/2020	12/1/2021	Leased/Rented Equipment \$500,000

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (Attach ACORD 101, Additional Remarks Schedule, if more space is required)

CERTIFICATE HOLDER Stantec Consulting Services Inc. 901 Ponce De Leon Boulevard Ste 900 Coral Gables, FL 33134	CANCELLATION SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS. AUTHORIZED REPRESENTATIVE R McGregor/KILLEN <i>[Signature]</i>
---	---

SECTION 00660


ACKNOWLEDGEMENT OF CONFORMANCE

WITH O.S.H.A. STANDARDS


TO THE INDIAN CREEK VILLAGE:

We, Giannetti Contracting Corporation, hereby acknowledge and agree that as Contractors for the construction of ROADWAY REDEVELOPMENT PROJECT, INDIAN CREEK VILLAGE, FLORIDA, that we have the sole responsibility for compliance with all requirements of the Federal Occupational Safety and Health Act of 1970, and all State and Local Safety and Health regulations, and agree to indemnify and hold harmless Indian Creek Village, and its Engineers, Architects and Landscape Architects against any and all legal liability or loss the Village, or the Engineer, Architect or Landscape Architect may incur due to

_____ failure to comply with such act.




ATTEST



ATTEST

Giannetti Contracting Corporation
CONTRACTOR

BY: 

Richard Gibbs III, NAME
President & Treasurer
January 20, 2021

DATE

END OF SECTION

SECTION 00665

TRENCH SAFETY ACT COMPLIANCE

Bidder acknowledges that the Florida Trench Safety Act, Section 553.60 et. seq. which became effective October 1, 1990, shall be in effect during the period of construction of the project. The Bidder, by signing and submitting the bids, in writing, assuring that it will perform any trench excavation in accordance with applicable trench safety standards. The Bidder further identifies the following separate item of costs of compliance with the applicable trench safety standards as well as the methods of compliance:

Methods of Compliance

Trench Slope / Box 29,768 Linear Feet @ \$1.25

(fill in methods)

Total \$ 37,210.00

Bidder acknowledges that this cost is included in the applicable items of the Proposal and in the Grand Total Bid Price. Failure to complete the above will result in the bid being declared non-responsive.


The Bidder is, and the Owner and Engineer are not, responsible to review or assess Bidder's safety precautions, programs or costs, or the means, methods, techniques or technique adequacy, reasonableness of cost, sequences or procedures of any safety precaution, program or cost, including but not limited to, compliance with any and all requirements of Florida Statute Section 553.60 et. seq. cited as the "Trench Safety Act". Bidder is, and the Owner and Engineer are not, responsible to determine if any safety or safety related standards apply to the project, including but not limited to, the "Trench Safety Act."

[Handwritten Signature]
Signature of Authorized Representative (Manual)

Richard Gibbs III, President & Treasurer
Name of Authorized Representative (Typed or Printed)

Sworn to and subscribed before me in the State and County first mentioned above on the 20th day of January, 2021


[Handwritten Signature] (affix seal)
Notary Public



My Commission Expires:

END OF SECTION

Ron DeSantis, Governor



Halsey Beshears, Secretary



**STATE OF FLORIDA
DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION**

CONSTRUCTION INDUSTRY LICENSING BOARD

THE GENERAL CONTRACTOR HEREIN IS CERTIFIED UNDER THE
PROVISIONS OF CHAPTER 489, FLORIDA STATUTES



APOSTOL, NICHOLAS JAMES

GIANNETTI CONTRACTING CORPORATION
1801 NW 18TH AVENUE
POMPANO BEACH FL 33069

LICENSE NUMBER: CGC1519762

EXPIRATION DATE: AUGUST 31, 2022


Always verify licenses online at MyFloridaLicense.com



Do not alter this document in any form.

This is your license. It is unlawful for anyone other than the licensee to use this document.

Ron DeSantis, Governor



Halsey Beshears, Secretary



STATE OF FLORIDA
DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION
CONSTRUCTION INDUSTRY LICENSING BOARD

THE UNDERGROUND UTILITY & EXCAVATION CO HEREIN IS CERTIFIED UNDER THE
PROVISIONS OF CHAPTER 489, FLORIDA STATUTES

LYSSENKO, ILIA V

GIANNETTI CONTRACTING CORPORATION
1801 NW 18 STREET
POMPANO BEACH FL 33069

LICENSE NUMBER: CUC1225383

EXPIRATION DATE: AUGUST 31, 2022


Always verify licenses online at MyFloridaLicense.com



Do not alter this document in any form.

This is your license. It is unlawful for anyone other than the licensee to use this document.

Ron DeSantis, Governor



Halsey Beshears, Secretary



STATE OF FLORIDA
DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION

CONSTRUCTION INDUSTRY LICENSING BOARD

THE PLUMBING CONTRACTOR HEREIN IS CERTIFIED UNDER THE
PROVISIONS OF CHAPTER 489, FLORIDA STATUTES

LYSSENKO, ILIA V

GIANNETTI CONTRACTING CORPORATION
1801 NW 18 STREET
POMPANO BEACH FL 33069

LICENSE NUMBER: CFC1429772

EXPIRATION DATE: AUGUST 31, 2022

Always verify licenses online at MyFloridaLicense.com



Do not alter this document in any form.

This is your license. It is unlawful for anyone other than the licensee to use this document.

BROWARD COUNTY LOCAL BUSINESS TAX RECEIPT

115 S. Andrews Ave., Rm. A-100, Ft. Lauderdale, FL 33301-1895 – 954-831-4000

VALID OCTOBER 1, 2020 THROUGH SEPTEMBER 30, 2021

DBA:
Business Name: GIANNETTI CONTRACTING CORPORATION

Receipt #: 180-271092
Business Type: GENERAL CONTRACTOR

Owner Name: NICHOLAS JAMES APOSTOL
Business Location: 1801 NW 18 ST
POMPANO BEACH
Business Phone: 9547928104

Business Opened: 08/12/2015
State/County/Cert/Reg: CGC1519762
Exemption Code:

Rooms **Seats** **Employees** **Machines** **Professionals**
6

Tax Amount	For Vending Business Only				Collection Cost	Total Paid
	Number of Machines:		Vending Type:			
	Transfer Fee	NSF Fee	Penalty	Prior Years		
27.00	0.00	0.00	0.00	0.00	0.00	27.00

THIS RECEIPT MUST BE POSTED CONSPICUOUSLY IN YOUR PLACE OF BUSINESS

**THIS BECOMES A TAX RECEIPT
WHEN VALIDATED**

This tax is levied for the privilege of doing business within Broward County and is non-regulatory in nature. You must meet all County and/or Municipality planning and zoning requirements. This Business Tax Receipt must be transferred when the business is sold, business name has changed or you have moved the business location. This receipt does not indicate that the business is legal or that it is in compliance with State or local laws and regulations.

Mailing Address:

GIANNETTI CONTRACTING CORPORATION
6340 SIMS DR
STERLING HEIGHTS, MI
48313

Receipt # WWW-19-00206219
Paid 08/27/2020 27.00

2020 - 2021

BROWARD COUNTY LOCAL BUSINESS TAX RECEIPT

115 S. Andrews Ave., Rm. A-100, Ft. Lauderdale, FL 33301-1895 – 954-831-4000

VALID OCTOBER 1, 2020 THROUGH SEPTEMBER 30, 2021

DBA:
Business Name: GIANNETTI CONTRACTING CORPORATION

Receipt #: 180-271092
Business Type: GENERAL CONTRACTOR

Owner Name: NICHOLAS JAMES APOSTOL
Business Location: 1801 NW 18 ST
POMPANO BEACH
Business Phone: 9547928104

Business Opened: 08/12/2015
State/County/Cert/Reg: CGC1519762
Exemption Code:

Rooms **Seats** **Employees** **Machines** **Professionals**
6

Signature	For Vending Business Only				Collection Cost	Total Paid
	Number of Machines:		Vending Type:			
	Transfer Fee	NSF Fee	Penalty	Prior Years		
	0.00	0.00	0.00	0.00	0.00	27.00

Receipt # WWW-19-00206219
Paid 08/27/2020 27.00

BROWARD COUNTY LOCAL BUSINESS TAX RECEIPT

115 S. Andrews Ave., Rm. A-100, Ft. Lauderdale, FL 33301-1895 – 954-831-4000
VALID OCTOBER 1, 2020 THROUGH SEPTEMBER 30, 2021

DBA:
Business Name: GIANNETTI CONTRACTING CORP

Receipt #: 189-285324
Business Type: ALL OTHER TYPES CONTRACTOR
 (CERT UNDERGROUND & EXCAV CNTR)

Owner Name: ILIA V LYSSENKO
Business Location: 1801 NW 18 ST
 POMPANO BEACH
Business Phone: 954-972-8104

Business Opened: 07/18/2017
State/County/Cert/Reg: CUC1225383
Exemption Code:

Rooms Seats Employees Machines Professionals
 50

Tax Amount	For Vending Business Only				Prior Years	Collection Cost	Total Paid
	Number of Machines:		Vending Type:				
	Transfer Fee	NSF Fee	Penalty				
135.00	0.00	0.00	0.00	0.00	0.00	0.00	135.00

THIS RECEIPT MUST BE POSTED CONSPICUOUSLY IN YOUR PLACE OF BUSINESS

THIS BECOMES A TAX RECEIPT

This tax is levied for the privilege of doing business within Broward County and is non-regulatory in nature. You must meet all County and/or Municipality planning and zoning requirements. This Business Tax Receipt must be transferred when the business is sold, business name has changed or you have moved the business location. This receipt does not indicate that the business is legal or that it is in compliance with State or local laws and regulations.

WHEN VALIDATED

Mailing Address:

GIANNETTI CONTRACTING CORP
 1801 NW 18 ST
 POMPANO BEACH, FL 33069

Receipt # WWW-19-00206219
Paid 08/27/2020 135.00

2020 - 2021

BROWARD COUNTY LOCAL BUSINESS TAX RECEIPT

115 S. Andrews Ave., Rm. A-100, Ft. Lauderdale, FL 33301-1895 – 954-831-4000
VALID OCTOBER 1, 2020 THROUGH SEPTEMBER 30, 2021

DBA:
Business Name: GIANNETTI CONTRACTING CORP

Receipt #: 189-285324
Business Type: ALL OTHER TYPES CONTRACTOR
 (CERT UNDERGROUND & EXCAV CNTR)

Owner Name: ILIA V LYSSENKO
Business Location: 1801 NW 18 ST
 POMPANO BEACH
Business Phone: 954-972-8104

Business Opened: 07/18/2017
State/County/Cert/Reg: CUC1225383
Exemption Code:

Rooms Seats Employees Machines Professionals
 50

Signature	For Vending Business Only				Prior Years	Collection Cost	Total Paid
	Number of Machines:		Vending Type:				
	Transfer Fee	NSF Fee	Penalty				
	0.00	0.00	0.00	0.00	0.00	0.00	135.00

Receipt # WWW-19-00206219
Paid 08/27/2020 135.00

BROWARD COUNTY LOCAL BUSINESS TAX RECEIPT

115 S. Andrews Ave., Rm. A-100, Ft. Lauderdale, FL 33301-1895 – 954-831-4000

VALID OCTOBER 1, 2020 THROUGH SEPTEMBER 30, 2021

DBA:
Business Name: GIANNETTI CONTRACTING CORP

Receipt #: 189-285324
Business Type: ALL OTHER TYPES CONTRACTOR
(CERT UNDERGROUND & EXCAV CNTR)

Owner Name: ILIA V LYSSENKO
Business Location: 1801 NW 18 ST
POMPANO BEACH
Business Phone: 954-972-8104

Business Opened: 07/18/2017
State/County/Cert/Reg: CUC1225383
Exemption Code:

Rooms Seats Employees Machines Professionals
50

For Vending Business Only						
Number of Machines:				Vending Type:		
Tax Amount	Transfer Fee	NSF Fee	Penalty	Prior Years	Collection Cost	Total Paid
135.00	0.00	0.00	0.00	0.00	0.00	135.00

THIS RECEIPT MUST BE POSTED CONSPICUOUSLY IN YOUR PLACE OF BUSINESS

THIS BECOMES A TAX RECEIPT
WHEN VALIDATED

This tax is levied for the privilege of doing business within Broward County and is non-regulatory in nature. You must meet all County and/or Municipality planning and zoning requirements. This Business Tax Receipt must be transferred when the business is sold, business name has changed or you have moved the business location. This receipt does not indicate that the business is legal or that it is in compliance with State or local laws and regulations.

Mailing Address:

GIANNETTI CONTRACTING CORP
1801 NW 18 ST
POMPANO BEACH, FL 33069

Receipt #WWW-19-00206219
Paid 08/27/2020 135.00

2020 - 2021

BROWARD COUNTY LOCAL BUSINESS TAX RECEIPT

115 S. Andrews Ave., Rm. A-100, Ft. Lauderdale, FL 33301-1895 – 954-831-4000

VALID OCTOBER 1, 2020 THROUGH SEPTEMBER 30, 2021

DBA:
Business Name: GIANNETTI CONTRACTING CORP

Receipt #: 189-285324
Business Type: ALL OTHER TYPES CONTRACTOR
(CERT UNDERGROUND & EXCAV CNTR)

Owner Name: ILIA V LYSSENKO
Business Location: 1801 NW 18 ST
POMPANO BEACH
Business Phone: 954-972-8104

Business Opened: 07/18/2017
State/County/Cert/Reg: CUC1225383
Exemption Code:

Rooms Seats Employees Machines Professionals
50

Signature	For Vending Business Only					
	Number of Machines:			Vending Type:		
Tax Amount	Transfer Fee	NSF Fee	Penalty	Prior Years	Collection Cost	Total Paid
135.00	0.00	0.00	0.00	0.00	0.00	135.00

Receipt #WWW-19-00206219
Paid 08/27/2020 135.00



[Department of State](#) / [Division of Corporations](#) / [Search Records](#) / [Search by Entity Name](#) /

Detail by Entity Name

Florida Profit Corporation
GIANNETTI CONTRACTING CORPORATION

Filing Information

Document Number	P07000058861
FEI/EIN Number	38-2477625
Date Filed	05/16/2007
State	FL
Status	ACTIVE
Last Event	AMENDMENT
Event Date Filed	10/23/2015
Event Effective Date	NONE

Principal Address

1801 NW 18TH ST
POMPANO BEACH, FL 33069

Changed: 01/12/2015

Mailing Address

1801 NW 18th ST
POMPANO BEACH, FL 33069

Changed: 02/15/2018

Registered Agent Name & Address

GIBBS, RICHARD
1801 NW 18TH ST
POMPANO BEACH, FL 33069

Name Changed: 10/23/2015

Address Changed: 01/12/2015

Officer/Director Detail

Name & Address

Title PT

GIBBS, RICHARD
1801 NW 18TH ST
POMPANO BEACH, FL 33069

Title VS

APOSTOL, NICHOLAS J
6340 SIMS ROAD
STERLING HEIGHTS, MI 48313

Annual Reports

Report Year	Filed Date
2018	02/15/2018
2019	01/09/2019
2020	01/20/2020

Document Images

01/20/2020 -- ANNUAL REPORT	View image in PDF format
01/09/2019 -- ANNUAL REPORT	View image in PDF format
02/15/2018 -- ANNUAL REPORT	View image in PDF format
08/30/2017 -- ANNUAL REPORT	View image in PDF format
03/15/2016 -- ANNUAL REPORT	View image in PDF format
10/23/2015 -- Amendment	View image in PDF format
01/12/2015 -- ANNUAL REPORT	View image in PDF format
01/17/2014 -- ANNUAL REPORT	View image in PDF format
09/09/2013 -- AMENDED ANNUAL REPORT	View image in PDF format
02/07/2013 -- AMENDED ANNUAL REPORT	View image in PDF format
01/09/2013 -- ANNUAL REPORT	View image in PDF format
01/04/2012 -- ANNUAL REPORT	View image in PDF format
01/06/2011 -- ANNUAL REPORT	View image in PDF format
05/11/2010 -- ANNUAL REPORT	View image in PDF format
02/18/2010 -- ANNUAL REPORT	View image in PDF format
04/01/2009 -- ANNUAL REPORT	View image in PDF format
01/14/2008 -- ANNUAL REPORT	View image in PDF format
06/04/2007 -- Name Change	View image in PDF format
05/16/2007 -- Domestic Profit	View image in PDF format



Florida Department of Transportation

RON DESANTIS
GOVERNOR

605 Suwannee Street
Tallahassee, FL 32399-0450

KEVIN J. THIBAUT, P.E.
SECRETARY

March 26, 2019

GIANNETTI CONTRACTING CORPORATION
1801 NW 18TH STREET
POMPANO BEACH, FLORIDA 33069

RE: CERTIFICATE OF QUALIFICATION

Dear Sir/Madam:

The Department of Transportation has qualified your company for the type of work indicated below. Unless your company is notified otherwise, this Certificate of Qualification will expire 5/30/2020. However, the new application is due 3/31/2020.

In accordance with S.337.14 (1) F.S. your next application must be filed within (4) months of the ending date of the applicant's audited annual financial statements.

If your company's maximum capacity has been revised, you can access it by logging into the Contractor Prequalification Application System via the following link:
[HTTPS://fdotwpl.dot.state.fl.us/ContractorPreQualification/](https://fdotwpl.dot.state.fl.us/ContractorPreQualification/)

Once logged in, select "View" for the most recently approved application, and then click the "Manage" and "Application Summary" tabs.

FDOT APPROVED WORK CLASSES:
DRAINAGE, GRADING, WATER MAINS, SEWER

You may apply for a Revised Certificate of Qualification at any time prior to the expiration date of this certificate according to Section 14-22.0041(3), Florida Administrative Code (F.A.C.), by accessing your most recently approved application as shown above and choosing "Update" instead of "View." If certification in additional classes of work is desired, documentation is needed to show that your company has done such work with your own forces and equipment or that experience was gained with another contractor and that you have the necessary equipment for each additional class of work requested.

All prequalified contractors are required by Section 14-22.006(3), F.A.C., to certify their work underway monthly in order to adjust maximum bidding capacity to available bidding capacity. You can find the link to this report at the website shown above.

Sincerely,

Alan Autry, Manager
Contracts Administration Office

AA:cj

**GIANNETTI CONTRACTING CORPORATION
CURRENT AND PENDING PROJECTS**

**VENETIAN PARKWAY WATER & SANITARY SEWER RELOCATION
OWNER: CITY OF VENICE, 401 WEST VENICE AVE., VENICE, FL. 34285
ENGINEER: ATKINS**

AWARDED: OCTOBER 2019 DAYS COMPLETION: 575 CONTRACT AMOUNT: \$3,346,844.00
SCOPE OF WORK: INSTALL 11,100 LF OF WATER MAINS, 21,000 LF OF GRAVITY SEWER MAINS, CONCRETE, SWALES, LANDSCAPING, DRIVEWAYS, AND ASSOCIATED RESTORATION. PIPE DIAMETERS ON SEWER PROJECT RANGED FROM 6" TO 8" AND WATER MAIN RANGED FROM 1" TO 6".

**OLEAN BLVD. WIDENING
OWNER: CHARLOTTE COUNTY, 18500 MURDOCK CIRCLE, SUITE 344, PORT CHARLOTTE, FL. 33948
ENGINEERS: GIFFELS-WEBSTER ENGINEERS, JOHNSON ENGINEERING, CHARLOTTE COUNTY PUBLIC WORKS
AWARDED: SEPTEMBER 2019 DAYS COMPLETION: 548 CONTRACT AMOUNT: \$16,241,354.58**

SCOPE OF WORK: INSTALL 12,000 LF OF WATER MAINS, 9,000 LF OF GRAVITY SEWER MAINS, 15,000 LF OF DRAINAGE, 4,700 LF OF FORCE MAIN, 10,700 LF OF RECLAIM WATER MAIN, 40,000 SY OF NEW ROAD RECONSTRUCTION, CONCRETE, SWALES, LANDSCAPING, IRRIGATION, DRIVEWAYS, SIGNALIZATION, LIGHTING, AND ASSOCIATED RESTORATION. PROJECT INCLUDES PIPE INSTALLATION OPEN CUT AND DIRECTIONAL DRILLED. PIPE DIAMETERS ON PROJECT RANGE FROM 4" TO 60".

**UTILITY ANALYSIS ZONE 110-111
OWNER: BROWARD COUNTY, 115 S. ANDREWS AVE., ROOM 212, FORT LAUDERDALE, FL. 33301
ENGINEER: CHEN MOORE & ASSOCIATES**

AWARDED: MARCH 2019 DAYS COMPLETION: 810 CONTRACT AMOUNT: \$25,859,999.10
SCOPE OF WORK: INSTALL 66,000 LF OF WATER MAINS, 50,000 LF OF GRAVITY SEWER MAINS, 160,000 SY OF NEW ROAD RECONSTRUCTION, CONCRETE, SWALES, LANDSCAPING, DRIVEWAYS, GUARDRAIL, AND ASSOCIATED RESTORATION. PROJECT INCLUDES PIPE INSTALLATION OPEN CUT, DIRECTIONAL DRILLED, AND PIPE BURSTING. PIPE DIAMETERS ON PROJECT RANGE FROM 4" TO 24".

**UTILITY ANALYSIS ZONE 123
OWNER: BROWARD COUNTY, 115 S. ANDREWS AVE., ROOM 212, FORT LAUDERDALE, FL. 33301
ENGINEER: CRAVEN THOMPSON & ASSOCIATES, INC**

AWARDED: JULY 2020 DAYS COMPLETION: 607 CONTRACT AMOUNT: \$15,347,000.00
SCOPE OF WORK: INSTALL 33,900 LF OF WATER MAINS, 27,900 LF OF GRAVITY SEWER MAINS, 5,900 LF OF FORCE MAINS, 65,000 SY OF NEW ROAD RECONSTRUCTION, CONCRETE, SWALES, LANDSCAPING, DRIVEWAYS, AND ASSOCIATED RESTORATION. PROJECT INCLUDES PIPE INSTALLATION IS OPEN CUT. PIPE DIAMETERS ON PROJECT RANGE FROM 4" TO 24".

**PEACE RIVER WATER MAIN INTERCONNECT
OWNER: SARASOTA COUNTY, 1660 RINGLING BLVD., 3RD FLOOR, SUITE 388B, SARASOTA, FL. 34236
ENGINEER: KIMLEY-HORN AND ASSOCIATES, INC.**

AWARDED: NOVEMBER 2020 DAYS COMPLETION: 540 CONTRACT AMOUNT: \$9,952,406.74
SCOPE OF WORK: INSTALL 28,000 LF OF 30" WATER MAIN INCLUDING 3,300 LF OF 30" DIRECTIONAL DRILL. ONE DRILL IS 1,100 LF IN LENGTH UNDER INTERSTATE 75 (I-75). PROJECT ALSO INCLUDES 42" JACK & BORE, 23,000 LF OF 3" CONDUIT, AND TIE INTO EXISTING TREATMENT PLANT. TREATMENT PLANT WORK INCLUDES CHEMICAL INJECTION IMPROVEMENTS, INSTRUMENT AND CONTROL IMPROVEMENTS, AND TIE IN TO WATER STORAGE TANKS. WORK INCLUDES ALL ASSOCIATED RESTORATION.

Giannetti Contracting Corporation

Reference Project

Name/Address:


Jones Loop Force Main, Punta Gorda, Florida

Name(s) and role(s) of key personnel working on this reference project:

Iliya Lyssenko - Project Manager, Howard Spurrier – Project Superintendent

Reference Project Description:

Project included over 9,300 LF of 16" and 900 LF of 12" Fusible PVC. Project quantities included seven 16" Directional Drills crossing multiple highways including Interstate 75 (I-75) totaling 3,535 LF. Project also included 20" Jack and Bore, Lift Station, and Associated Restoration.

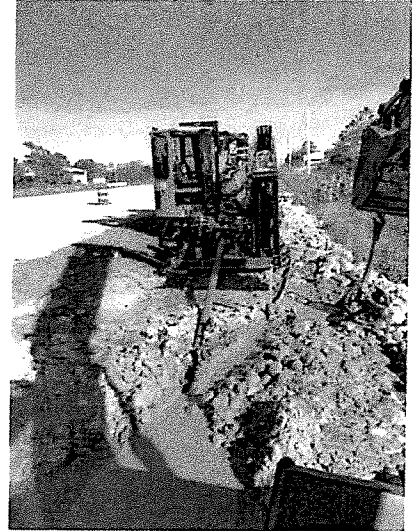

Scope of Services Provided: **Construction**

Construction Start Date: **February 2019**

Construction Completion Date: **March 2020**

Project Construction Cost: **\$2,070,882.38**

Reference Company Name: **City of Punta Gorda**

Reference Name: **Robert Ruth, Utilities Project Manager**

Reference Phone Number: **(941) 575-5054** Fax Number:

E-mail: rruth@cityofpuntagordafl.com

Giannetti Contracting Corporation

Reference Project

Name/Address:


Yacht Harbor Manor Roadway Project, Riviera Beach, Florida

Name(s) and role(s) of key personnel working on this reference project:

Ilia Lyssenko - Project Manager, Jeffrey Melnechuk – Project Superintendent

Reference Project Description:

Neighborhood infrastructure improvements on Singer Island in Riviera Beach, Florida. This neighborhood project includes over 8,500 LF of water main, 168 water services, 7,800 LF of Gravity Sewer (up to 14' deep), 168 sewer laterals, 900 LF of force main, 8,400 LF storm drainage, and 21,000 SY of new concrete road construction. Project also included new swales, driveways, and curbing.

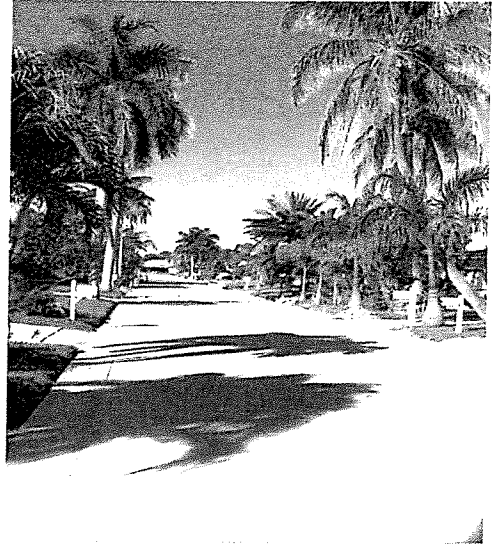

Scope of Services **Construction**
Provided:

Construction Start **November 2017**
Date:

Construction Completion Date: **November 2019**

Project Construction **\$8,642,718.50**
Cost:

Reference Company **City of Riviera Beach,**
Name: **Florida**

Reference **Terrence N. Bailey, PE, Interim Director of Public Works**
Name:

Reference Phone **(561) 845-4080** Fax
Number: Number:

E-mail: tbailey@rivierabeach.org

Giannetti Contracting Corporation

Reference Project Name/Address:


**Water Main Replacement Program – Hollywood Blvd. to Sheridan St., Federal Hwy. to Intracoastal Waterway.
Hollywood, Florida**

Name(s) and role(s) of key personnel working on this reference project:

Iliia Lyssenko - Project Manager, Jeff Melnechuk – Project Superintendent

Reference Project Description:

The Water Main Replacement Program – Hollywood Blvd. to Sheridan St. Federal Hwy. to the Intracoastal Waterway Project is located in the City of Hollywood and is located South of Sheridan St., North of Hollywood Blvd. East of Federal Hwy., and West of the Intracoastal Waterway. The infrastructure improvements to the existing neighborhood included new water main and drainage. This neighborhood project includes over 116,000 LF of new water main and 945 water services and over 3,400 LF of new drainage. Main line pipe sizes ranged from 4" to 48" in diameter. Project also included over 217,000 SY of mill & overlay, sidewalks, and driveway aprons.

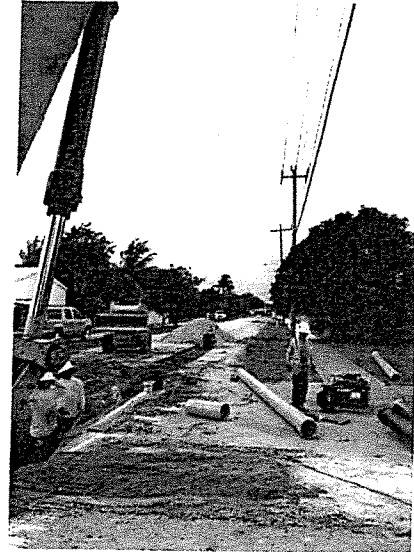

Scope of Services Provided: **Construction**

Construction Start Date: **November 2015**

Construction Completion Date: **August 2018**

Project Construction Cost: **\$13,689,489.38**

Reference Company Name: **City of Hollywood**

Reference Name: **Mr. Clece Aurelus, PE, Senior Project Manager**

Reference Phone Number: **(954) 967-4455**

Fax Number: **(954) 967-4450**

E-mail: caurelus@hollywoodfl.org

Giannetti Contracting Corporation

Reference Project
Name/Address:

Jupiter Inlet Colony Neighborhood Rehabilitation Project, Jupiter Inlet Colony, Fl.

Name(s) and role(s) of key personnel working on this reference project:

Iliya Lyssenko - Project Manager, Tim Gibbs – Project Superintendent

Reference Project Description:

Neighborhood infrastructure improvements on island in Jupiter Inlet Colony, Florida. This neighborhood project includes over 16,000 LF of water main, 412 water services, 14,000 LF of Gravity Sewer (up to 20' deep), 243 sewer laterals, lift station, 2,600 LF of force main, 7,200 LF storm drainage, and 33,200 SY of new road construction. Project also included new swales, driveways, and curbing.



Scope of Services Provided: **Construction**

Construction Start Date: **June 2016**

Construction Completion Date: **April 2018**

Project Construction Cost: **\$8,912,466.41**

Reference Company Name: **Kimley Horn / Arcadis U.S.**

Reference Name: **Tom Jensen, Project Engineer/Construction Manager**

Reference Phone Number: **(561) 248-5967** Fax Number:

E-mail: **tom.jensen@kimley-horn.com**

Giannetti Contracting Corporation

Reference Project Name/Address:


Cudjoe Regional Wastewater Inner Islands Collection System and Transmission System

Name(s) and role(s) of key personnel working on this reference project:

Iliya Lyssenko - Project Manager, Tim Gibbs – Project Superintendent, Tony Donofrio – Project Superintendent

Reference Project Description:

Cudjoe Regional Wastewater Inner Islands Project in Cudjoe, Upper Sugarloaf, and Summerland Keys, Florida is an environmentally sensitive sewer replacement project. The Cudjoe Project includes over 4,000 LF of new water main, 99,000 LF of gravity sewer, 1,783 sewer laterals, 32 area lift stations, 157,000 LF of force main, 416 grinder pump stations, 2 bridge crossings, and 2 master lift stations. Main line pipe sizes ranged from 2" to 16" in diameter. Project also included over 200,000 SY of overlay.

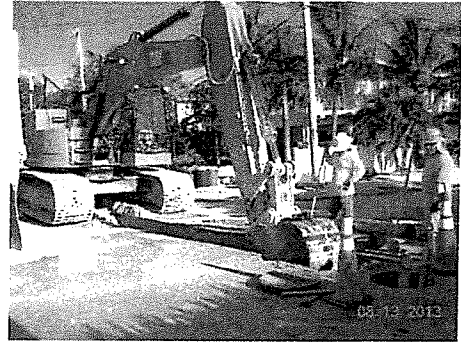

Scope of Services
Provided:

Construction

Construction Start Date: **March 2013**

Construction Completion Date: **October 2015**

Project Construction Cost: **\$42,486,386.**

Reference Company Name: **Florida Keys Aqueduct
Authority**

Reference Name: **Tom Walker, PE, Executive Director**

Reference Phone Number: **(305) 295-2205** Fax
Number:

E-mail: **twalker@fkaa.com**

Giannetti Contracting Corporation

Reference Project Name/Address:

Big Coppitt Wastewater Collection System Contract 2 – Rockland & Geiger Key, Florida

Name(s) and role(s) of key personnel working on this reference project:

Richard Gibbs - Project Manager, Jeff Melnechuk – Project Superintendent

Reference Project Description:

The Big Coppitt Wastewater Collection System Contract 2 Project in Rockland and Geiger Key, Florida is an environmentally sensitive water and sewer replacement project. The Big Coppitt Project included over 24,000 LF of new water main, 297 water services, 40,000 LF of gravity sewer, seven lift stations, 9,900 LF of force main, and one bridge crossing. Main line pipe sizes ranged from 4" to 8" in diameter. Project also included over 76,000 SY of mill & overlay.



Scope of Services Provided: **Construction**

Construction Start Date: **June 2008**

Construction Completion Date: April 2010

Project Construction Cost: **\$9,667,750.16**

Reference Company Name: **Florida Keys Aqueduct Authority**

Reference Name: **Tom Walker, PE, Executive Director**

Reference Phone Number: **(305) 295-2205** Fax Number:

E-mail: twalker@fkaa.com

Giannetti Contracting Corporation

Reference Project Name/Address:

Cudjoe Regional Wastewater Outer Islands Collection System and Transmission System

Name(s) and role(s) of key personnel working on this reference project:

Iliia Lyssenko - Project Manager, Tim Gibbs – Project Superintendent, Tony Donofrio – Project Superintendent

Reference Project Description:

Cudjoe Regional Wastewater Outer Islands Project in Lower Sugarloaf, Ramrod, Middle Torch, Big Torch, Little Torch, Big Pine, and No Name Keys, Florida is an environmentally sensitive sewer replacement project. Giannetti's scope of the Cudjoe Outer Islands Project includes over 30,000 LF of new water main, 469 Water Services, 52,000 LF of gravity sewer, 707 sewer laterals, 18 area lift stations, 18,000 LF of force main. Main line pipe sizes ranged from 2" to 18" in diameter.



Scope of Services Provided: **Construction**

Construction Start Date: **May 2014** Construction Completion Date: **December 2016**

Project Construction Cost: **\$16,547,743.60 (Giannetti Scope)**

Reference Company Name: **FCAA, Owner** Reference Name: **Tom Walker, PE, Executive Director**

**Subcontractor for Reynolds
Construction, (formerly)
Layne Heavy Civil**

Reference Phone Number: **(305) 295-2205** Fax Number: **N/A** E-mail: **twalker@fcaa.com**

Giannetti Contracting Corporation

Reference Project

Name/Address:


SW 18th Street Roadway Reconstruction and 16 Inch Water Main Extension, Boca Raton, Florida

Name(s) and role(s) of key personnel working on this reference project:

Bob Henning - Project Manager, Tony D'Onofrio – Project Superintendent

Reference Project Description:

Roadway Utility project in Boca Raton, Florida. Project included over 2,000 LF of 16" Water Main including hanging pipe on existing bridge and also 30" Jack and Bore under FEC Railroad, new road construction, concrete sidewalks and curbs, and restoration.

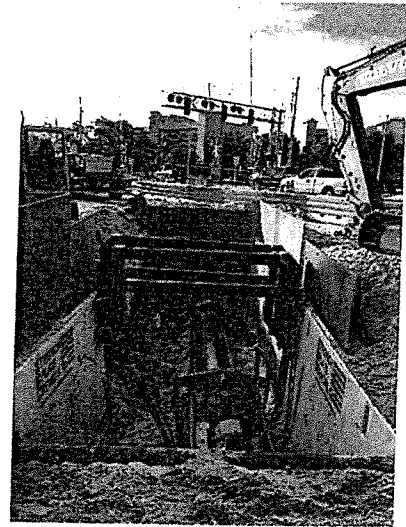

Scope of Services Provided: **Construction**

Construction Start Date: **March 2018**

Construction Completion Date: **December 2018**

Project Construction Cost: **\$1,608,710**

Reference Company Name: **LDI /Arcadis U.S., Inc.**

Reference Name:

Robert (Bo) Moyer

Reference Phone Number: **(561) 352-0280**

Fax Number: ()

E-mail:

bo.moyer@yahoo.com

Giannetti Contracting Corporation

Reference Project Name/Address:

Water Main Replacement Program – Sheridan St. to Pershing St., N. 22nd Ave. to N. 24th Ave. Hollywood, Florida

Name(s) and role(s) of key personnel working on this reference project:

Ilia Lyssenko - Project Manager, Jeff Melnechuk – Project Superintendent


Reference Project Description:

The Water Main Replacement Program – Sheridan St. to Pershing St. N. 22nd Ave. to N. 24th Ave. Project is located in the City of Hollywood and is located South of Pershing St., North of Sheridan St., East of N. 24th Ave., and West of N. 22nd Ave. The infrastructure improvements to the existing neighborhood included new water main.

This water main replacement program project included over 28,500 LF of new water main and 356 water services.

Main line pipe sizes ranged from 4" to 8" in diameter.

Project also includes over 46,000 SY of mill & overlay, sidewalks, and driveway aprons.

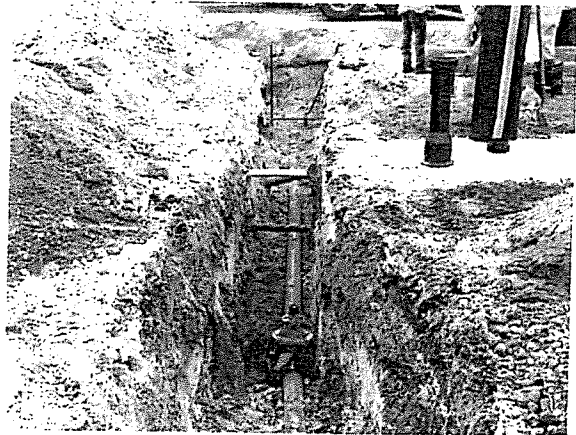

Scope of Services Provided: **Construction**

Construction Start Date: **September 2015**

Estimated Construction Completion Date:

December 2016

Project Construction Cost: **\$2,868,708.00**

Reference Company Name: **City of Hollywood**

Reference Name: **Mr. Clece Aurelus, PE, Senior Project Manager**

Reference Phone Number: **(954) 967-4455**

Fax Number: **(954) 967-4450**

E-mail: caurelus@hollywoodfl.org

Giannetti Contracting Corporation

Reference Project Name/Address:

Water Main Replacement Program - N. 72nd Ave. to N. 76th Ave. Polk St. to Johnson St. , Hollywood, Florida

Name(s) and role(s) of key personnel working on this reference project:

Ilia Lyssenko - Project Manager, Jeff Melnechuk – Project Superintendent

Reference Project Description:

The Water Main Replacement Program – N. 72nd Ave. to N. 76th Ave. Polk St. to Johnson St. Project is located in the City of Hollywood and is located South of Johnson St., North of Polk St., East of N. 76th Ave., and West of N. 72nd Ave. The infrastructure improvements to the existing neighborhood included new water main. This water main replacement program project included over 27,000 LF of new water main and 605 water services. Main line pipe sizes ranged from 6" to 12" in diameter. Project also included over 75,000 SY of mill & overlay, sidewalks, driveway aprons, and sodded swales.



Scope of Services **Construction**
Provided:

Construction Start Date: **September 2014**

Construction Completion Date: **August 2015**

Project Construction Cost: **\$3,684,607.50**

Reference Company Name: **City of Hollywood**

Reference Name: **Mr. Clece Aurelus, PE, Senior Project Manager**

Reference Phone Number: **(954) 967-4455**

Fax Number: **(954) 967-4450**

E-mail: caurelus@hollywoodfl.org

Giannetti Contracting Corporation

Reference Project Name/Address:


North County Neighborhood Improvement Project – Bid Package 11, (NE) Northeast Quadrant, Pompano Beach, Florida

Name(s) and role(s) of key personnel working on this reference project:

Pat Sweet - Project Manager, Jeff Melnechuk – Project Superintendent

Reference Project Description:

The North County Neighborhood Improvement Project (NCNIP) Northeast Quadrant includes approximately 720 acres of land between Dixie Highway and Federal Highway, North of Sample Road in Pompano Beach. This area is primarily residential, built in the 1950's and early 1960's. The area was developed with limited sanitary sewer system, no drainage and an inadequate water distribution system. NCNIP Bid Package 11 included over 29,350 LF of new drainage, 64,000 LF of water main, 553 Water Services, 49,700 LF of reclaimed water main, 796 reclaimed water services, 43,805 LF of gravity sewer main, 750 sewer laterals, lift station, and 1,630 LF of force main. Main line pipe sizes ranged from 4" to 48" in diameter. Project also included over 124,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales.

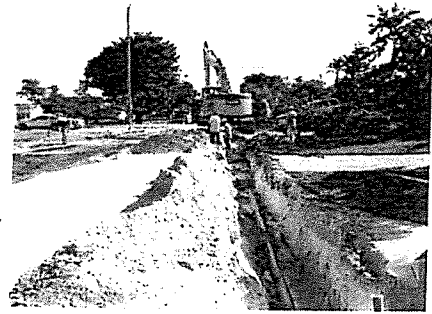

Scope of Services Provided: **Construction**

Construction Start Date: **October 2011**

Construction Completion Date: **December 2014**

Project Construction Cost: **\$17,807,186.24**

Reference Company Name: **Broward County Water & Wastewater Services**

Reference Name: **Mr. Patrick MacGregor, Expansion Administrator**

Reference Phone Number: **(954) 831-0904**

Fax Number: **(954) 831-0798**

E-mail: **pamacgregor@broward.org**

Giannetti Contracting Corporation

Reference Project Name/Address:


Water Main Replacement Program – Hollywood Blvd. to Johnson St. N. 46th Ave. to N. 52nd Ave. Hollywood, Florida

Name(s) and role(s) of key personnel working on this reference project:

Iliia Lyssenko - Project Manager, Jeff Melnechuk – Project Superintendent

Reference Project Description:

The Water Main Replacement Program – Hollywood Blvd. to Johnson St. N. 46th Ave. to N. 52nd Ave. Project is located in the City of Hollywood and is located South of Johnson St., North of Hollywood Blvd., East of N. 52nd Ave., and West of N. 46th Ave. The infrastructure improvements to the existing neighborhood included new water main. This water main replacement program project included over 27,000 LF of new water main and 150 water services. Main line pipe sizes ranged from 4" to 12" in diameter. Project also included over 36,000 SY of mill & overlay, sidewalks, driveway aprons, and sodded swales.

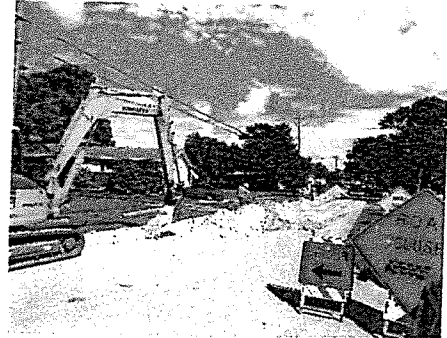

Scope of Services Provided: **Construction**

Construction Start Date: **June 2013**

Construction Completion Date: **May 2014**

Project Construction Cost: **\$2,132,773.26**

Reference Company Name: **City of Hollywood**

Reference Name: **Mr. Clece Aurelus, PE, Senior Project Manager**

Reference Phone Number: **(954) 967-4455**

Fax Number: **(954) 967-4450**

E-mail: caurelus@hollywoodfl.org

Giannetti Contracting Corporation

Reference Project Name/Address:

Belvedere Homes Infrastructure Improvements – Phase I , West Palm Beach, Florida

Name(s) and role(s) of key personnel working on this reference project:

Bob Henning - Project Manager, Jeff Melnechuk – Project Superintendent

Reference Project Description:

The Belvedere Homes Infrastructure – Phase I Project is located in the City of West Palm Beach and is located South of the LWDD L-2 Canal, North of Belvedere Road, East of Tallahassee Dr. and West of Congress Ave. The infrastructure improvements to the existing neighborhood included new water, drainage, and vacuum sewer. Belvedere Homes included over 15,100 LF of new water main, 177 water services, 5,700 LF of drainage, 13,900 LF of Vacuum Sewer, 176 Valve Pits, and 1,500 LF of force main. Main line pipe sizes ranged from 4” to 48” in diameter. Project also included over 16,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales.



Scope of Services Provided: **Construction**

Construction Start Date: **March 2012**

Construction Completion Date: **April 2013**

Project Construction Cost: **\$4,246,809.73**

Reference Company Name: **Palm Beach County Water Utilities**

Reference Name: **Joe Tanacredi, PE, Project Manager**

Reference Phone Number: **(561) 493-6088**

Fax Number:

E-mail: jtanacredi@pbcwater.com

Name of Firm (Design-Builder/A/E Sub-consultant/Non-A/E Sub-consultant/Sub-contractor):

Giannetti Contracting Corporation

Reference Project Name/Address:


Broadview Park Neighborhood Improvement Project – Bid Package 3, Fort Lauderdale, Florida

Name(s) and role(s) of key personnel working on this reference project:

Richard Gibbs - Project Manager, Jeff Melnechuk – Project Superintendent

Reference Project Description:

The Broadview Bid Package #3 Project is located in the City of Fort Lauderdale and is located South of Peters Rd./Davie Blvd., North of Interstate 595, East of Florida's Turnpike and West of State Rd. 7. The infrastructure improvements to the existing neighborhood included new sanitary sewer and drainage system. Bid Package #3 included over 20,000 LF of new drainage, 46,700 LF of gravity sewer main, 1,032 sewer laterals, lift station, and 6,200 LF of force main. Main line pipe sizes ranged from 8" to 24" in diameter. Project also included over 150,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales.

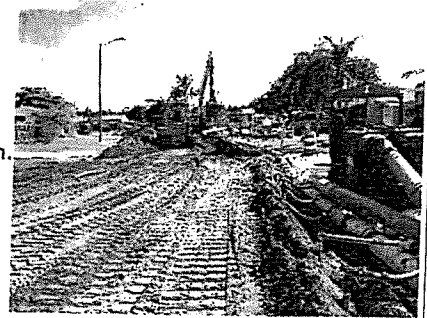

Scope of Services Provided: **Construction**

Construction Start Date: **September 2010**

Construction Completion Date: **March 2013**

Project Construction Cost: **\$13,261,559.24**

Reference Company Name: **Broward County Water & Wastewater Services**

Reference Name: **Mr. Patrick MacGregor, Expansion Administrator**

Reference Phone Number: **(954) 831-0904**

Fax Number: **(954) 831-0798**

E-mail: **pamacgregor@broward.org**

Giannetti Contracting Corporation

Reference Project Name/Address:

Utility Analysis Zone Improvement Program (UAZ) 308, Dania Beach, Florida

Name(s) and role(s) of key personnel working on this reference project:

Richard Gibbs - Project Manager, Jeff Melnechuk – Project Superintendent

Reference Project Description:

The UAZ 308 Project is located in the City of Dania Beach and is located South of Griffin Road, North of SW 52nd St., East of SW 29th Ter. and West of SW 27th Ave.. The infrastructure improvements to the existing neighborhood included new sanitary sewer and water distribution system. UAZ 308 included over 28,700 LF of water main, 219 Water Services, 20,300 LF of Gravity sewer main, 340 sewer laterals, and 1,270 LF of force main. Main line pipe sizes ranged from 6" to 10" in diameter. Project also included over 50,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales.



Scope of Services Provided: **Construction**

Construction Start Date: **June 2011**

Construction Completion Date: **January 2013**

Project Construction Cost: **\$6,249,174.96**

Reference Company Name: **Broward County Water & Wastewater Services**

Reference Name: **Mr. Patrick MacGregor, Expansion Administrator**

Reference Phone Number: **(954) 831-0904**

Fax Number: **(954) 831-0798**

E-mail: **pamacgregor@broward.org**

Giannetti Contracting Corporation

Reference Project Name/Address:


N-30 Canal Culvert Extension Project – Central Broward Water Control District

Name(s) and role(s) of key personnel working on this reference project:

Bob Henning - Project Manager, Tim Gibbs – Project Superintendent

Reference Project Description:

N-30 Canal Culvert Extension Project in Davie including clearing and drainage installation. Project consisted of over 2,500 LF of new reinforced concrete drainage pipe ranging from 15" to 60" diameter. Over 98% of the pipe on project was 60" RCP. Project also included rock excavation.

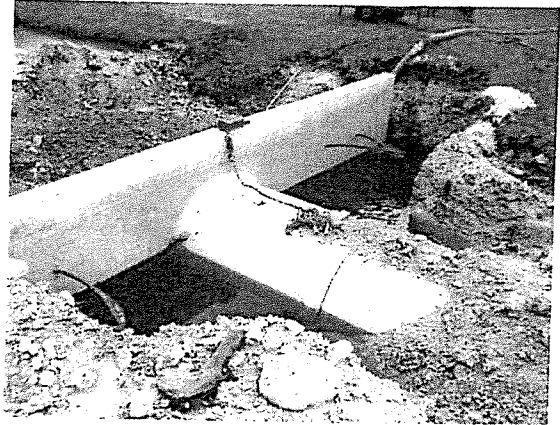

Scope of Services Provided: **Construction**

Professional Fees

Construction Start Date **July 2012**

Construction Completion Date: **December 2012**

Project Construction Cost: **\$ 747,018.15**

Reference Company Name: **Craven Thompson & Associates**

Reference Name: **Don Shaver, Director of Construction Management**

Reference Phone Number: **(954) 739 - 6400** Fax Number: **(954) 739 -6409** E-mail: dshaver@craventhompson.com

Giannetti Contracting Corporation

Reference Project Name/Address:

Utility Analysis Zone Improvement Program (UAZ) 307 & 315, Dania Beach, Florida

Name(s) and role(s) of key personnel working on this reference project:

Richard Gibbs - Project Manager, Jeff Melnechuk – Project Superintendent

Reference Project Description:

The UAZ 307 and 315 Projects are located in the City of Dania Beach and are located South of SW 42nd Street, North of Griffin Road, East of SW 38th Ave. and West of I-95. The infrastructure improvements to the existing neighborhood included new sanitary sewer and water distribution system. UAZ 307 & 315 included over 19,900 LF of water main, 228 Water Services, 16,800 LF of gravity sewer main, 350 sewer laterals, and 1,930 LF of force main. Main line pipe sizes ranged from 4" to 12" in diameter. Project also included over 36,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales



Scope of Services Provided: **Construction**

Construction Start Date: **November 2009**

Construction Completion Date: **November 2011**

Project Construction Cost: **\$5,949,866.26**

Reference Company Name: **Broward County Water & Wastewater Services**

Reference Name: **Mr. Patrick MacGregor,
Expansion Administrator**

Reference Phone Number: **(954) 831-0904**

Fax Number: **(954) 831-0798**

E-mail: **pamacgregor@broward.org**

Giannetti Contracting Corporation

Reference Project Name/Address:


Davie Blvd 54" F.M. along S.E. 10th Ave. to GTL – Package C, Fort Lauderdale, Florida

Name(s) and role(s) of key personnel working on this reference project:

Richard Gibbs - Project Manager, Jeff Melnechuk – Project Superintendent

Reference Project Description:

The Davie Blvd. 54" Force Main Project is Located in the City of Fort Lauderdale. The large diameter wastewater force main project included over 1,300 LF of 16" to 54" diameter force main with 340 LF being 54".

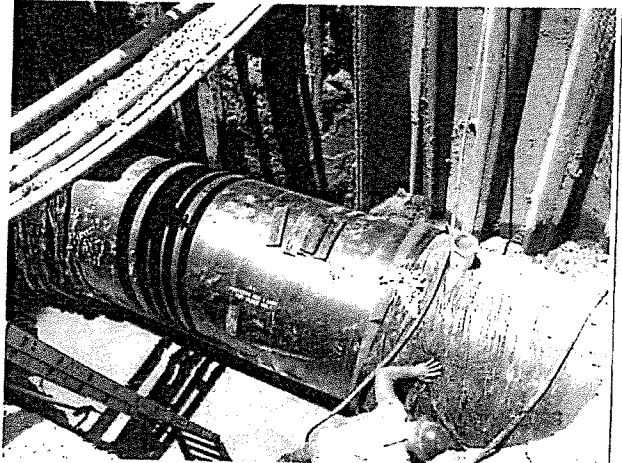

Scope of Services
Provided:

Construction

Construction Start Date: **July 2009**

Construction Completion Date: **March 2010**

Project Construction Cost: **\$2,033,576.56**

Reference Company Name: **City of Fort Lauderdale
Public Works Dept.**

Reference Name: **Mr. Jean Examond,
Project Manager II**

Reference Phone Number: **(954) 828-5772** Fax Number: **(954) 828-5074** E-mail: **jexamond@fortlauderdale.gov**

Richard Gibbs, III, President/Treasurer
1801 NW 18th STREET
POMPANO BEACH, FLORIDA 33069
Ph: 954-972-8104 Fax: 954-972-8108
richie@giannetticorp.com



Richard (Richie) Gibbs has over 24 years' construction experience as a project manager, estimator, superintendent, foreman, and general partner, in the underground construction industry with governmental agencies in Florida and Michigan. Richie also has experience in commercial construction including custom home building in Michigan and Florida over the past 21 years. Richie is "hands-on" with all current projects in the South Florida area.

EMPLOYMENT:

Giannetti Contracting Corp. 1995 – Present Chief Operating Officer/ President / Treasurer

RECENT PROJECTS:

City of Riviera Beach, Florida – Yacht Harbor Manor Roadway Project 2017-2019

Contract Amount: \$8,642,718.50

- Neighborhood infrastructure improvements project on island in Riviera Beach, Florida. Project included over 24,700 LF of water main, gravity sewer, and drainage from 6" to 24" in diameter. Project also included over 21,000 SY of new concrete roadway construction, curbs, driveway aprons, and sodded swales.

City of Punta Gorda, Florida – Jones Loop Force Main - 2019

Contract Amount: \$2,066,078.44

- Large diameter force main replacement project in Punta Gorda, Florida. Project consisted of over 10,000 LF of new force main with over 90% being 16" diameter. Project also consisted on multiple 16" directional drills with four drills being over 500 LF in length. Project also consisted of a jack & bore, lift station, and associated restoration.

City of Hollywood, Florida – Water Main Replacement Program – Hollywood Blvd. to Sheridan St., Federal Hwy. to Intracoastal Waterway 2015 - 2018

Contract Amount: \$12,253,900.57

- Water Main Replacement Project included over 116,000 LF of new water main and 3,400 LF of new drainage from 4" to 48" in diameter. Project also included over 217,000 SY of mill & overlay, sidewalks, driveway aprons, and sodded swales.

Loxahatchee River Environmental Control District – Jupiter Inlet Colony Neighborhood Rehabilitation Project - 2016 - 2018

Contract Amount: \$8,912,466.41

- Neighborhood infrastructure improvements project on island in Jupiter Inlet Colony, Florida. Project included over 39,000 LF of water main, gravity sewer force main, and drainage from 4" to 30" in diameter. New lift station was also installed. Project also included over 33,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales.

Florida Keys Aqueduct Authority – Cudjoe Inner Islands 2013 – 2015

Contract \$45,119,495.13.

- Environmentally sensitive complete sewer replacement for Cudjoe, Upper Sugarloaf, and Summerland Keys. The transmission main along US-1 is also being replaced from MM 19 to 25. Project includes over 300,000 LF of water main, low pressure force main, open cut force main, gravity sewer main, slip lining, and directional bores from 1-1/2" to 16" in diameter. Project also includes 31 area lift stations and 2 master lift stations and 200,000 SY of 1" Asphalt Overlay.

Broward County - North County Neighborhood Improvements Bid Pack # 11 - 2011 - 2014

Contract Amount: \$17,807,186.

- Project included over 188,000 LF of new drainage, water main, gravity sewer main, force main, reclaimed water main from 4” to 48” in diameter. Over 124,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

Palm Beach County Water Utilities Department – Belvedere Homes Phase 2 - 2012-2013

Contract Amount: \$ 4,252,998.

- Over 24,000 LF of new drainage, water main, and vacuum sewer main from 4” to 42” in diameter. Project also included 1” milling and overlay as well as over 16,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

Broward County - Utility Analysis Zone Improvement Program (UAZ) 308 - 2011-2013

Contract Amount: \$6,488,292.

- Project included over 50,000 LF of new water main, gravity sewer main, and force main from 6” to 10” in diameter. Over 50,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

Broward County – Broadview Park Neighborhood Improvement Project – Bid Pack #3 - 2010 - 2013

Contract Amount: \$13,261,559.

- Project included over 72,000 LF of new drainage, gravity sewer main, and force main from 8” to 24” in diameter. Over 150,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

LICENSES AND CERTIFICATIONS:

OSHA Qualified Person

Nicholas J. Apostol, V.P. / Secretary
1801 NW 18th STREET
POMPANO BEACH, FLORIDA 33069
Ph: 954-972-8104 Fax: 954-972-8108
nick@giannetticorp.com



Nick Apostol has over 30 years' underground utility construction experience with governmental agencies and also commercial vertical construction as project manager, estimator, superintendent, foreman, and general partner.

EMPLOYMENT:

Giannetti Contracting Corp. 1990 – Present Vice-President / Secretary

Oakland County Drain Commissioners
Oakland, MI 1988-1990 Construction Inspector

RECENT PROJECTS:

City of Riviera Beach, Florida – Yacht Harbor Manor Roadway Project 2017-2019

Contract Amount: \$8,642,718.50

- Neighborhood infrastructure improvements project on island in Riviera Beach, Florida. Project included over 24,700 LF of water main, gravity sewer, and drainage from 6” to 24” in diameter. Project also included over 21,000 SY of new concrete roadway construction, curbs, driveway aprons, and sodded swales.

City of Punta Gorda, Florida – Jones Loop Force Main - 2019

Contract Amount: \$2,066,078.44

- Large diameter force main replacement project in Punta Gorda, Florida. Project consisted of over 10,000 LF of new force main with over 90% being 16” diameter. Project also consisted on multiple 16” directional drills with four drills being over 500 LF in length. Project also consisted of a jack & bore, lift station, and associated restoration.

City of Hollywood, Florida – Water Main Replacement Program – Hollywood Blvd. to Sheridan St., Federal Hwy. to Intracoastal Waterway 2015 - 2018

Contract Amount: \$12,253,900.57

- Water Main Replacement Project included over 116,000 LF of new water main and 3,400 LF of new drainage from 4” to 48” in diameter. Project also included over 217,000 SY of mill & overlay, sidewalks, driveway aprons, and sodded swales.

Loxahatchee River Environmental Control District – Jupiter Inlet Colony Neighborhood Rehabilitation Project - 2016 - 2018

Contract Amount: \$8,912,466.41

- Neighborhood infrastructure improvements project on island in Jupiter Inlet Colony, Florida. Project included over 39,000 LF of water main, gravity sewer force main, and drainage from 4” to 30” in diameter. New lift station was also installed. Project also included over 33,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales.

Florida Keys Aqueduct Authority – Cudjoe Inner Islands 2013 – 2016

Contract \$45,119,495.13.

- Environmentally sensitive complete sewer replacement for Cudjoe, Upper Sugarloaf, and Summerland Keys. The transmission main along US-1 is also being replaced from MM 19 to 25. Project includes over 300,000 LF of water main, low pressure force main, open cut force main, gravity sewer main, slip lining, and directional bores from 1-1/2” to 16” in diameter. Project also includes 31 area lift stations and 2 master lift stations and 200,000 SY of 1” Asphalt Overlay.

Broward County - North County Neighborhood Improvements Bid Pack # 11 - 2011 - 2014

Contract Amount: \$17,807,186.

- Project included over 188,000 LF of new drainage, water main, gravity sewer main, force main, reclaimed water main from 4" to 48" in diameter. Over 124,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

Broward County - Utility Analysis Zone Improvement Program (UAZ) 308 - 2011-2013

Contract Amount: \$6,488,292.

- Project included over 50,000 LF of new water main, gravity sewer main, and force main from 6" to 10" in diameter. Over 50,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

Palm Beach County Water Utilities Department – Belvedere Homes Phase 2 – 2012 - 2013

Contract Amount: \$ 4,252,998.

- Over 24,000 LF of new drainage, water main, and vacuum sewer main from 4" to 42" in diameter. Project also included 1" milling and overlay as well as over 16,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

Broward County – Broadview Park Neighborhood Improvement Project – Bid Pack #3 - 2010 - 2013

Contract Amount: \$13,261,559.

- Project included over 72,000 LF of new drainage, gravity sewer main, and force main from 8" to 24" in diameter. Over 150,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

EDUCATION:

Central Michigan University, Bachelor of Science, Construction Technology, 1989,

LICENSES AND CERTIFICATIONS: Florida General Contractor, Michigan Licensed Residential Builder, OSHA Qualified Person, Florida Stormwater Inspector, ATTSA Florida Advanced

Jeffrey Melnechuk, Operations Manager
General Superintendent

1801 NW 18th STREET
POMPANO BEACH, FLORIDA 33069
Ph: 954-972-8104 Fax: 954-972-8108
mally@giannetticorp.com



Jeff (Mally) has over 21 years' underground utility construction experience with governmental agencies as superintendent, foreman, and operator in Michigan and Florida. Jeff's experience also includes residential and commercial vertical construction.

EMPLOYMENT:

Giannetti Contracting Corp. 1998 – Present Operations Manager / General Superintendent

RECENT PROJECTS:

Broward County - Utility Analysis Zone Improvement Program (UAZ) 110-111 – 2019-Present

Contract Amount: \$24,948,799.10

- Project includes over 115,000 LF of new water main, gravity sewer main, and drainage from 4" to 24" in diameter. Over 155,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

City of Hollywood, Florida – Water Main Replacement Program – Hollywood Blvd. to Sheridan St., Federal Hwy. to Intracoastal Waterway 2015 - 2018

Contract Amount: \$12,253,900.57

- Water Main Replacement Project included over 116,000 LF of new water main and 3,400 LF of new drainage from 4" to 48" in diameter. Project also included over 217,000 SY of mill & overlay, sidewalks, driveway aprons, and sodded swales.

Loxahatchee River Environmental Control District – Jupiter Inlet Colony Neighborhood Rehabilitation Project - 2016 - 2018

Contract Amount: \$8,912,466.41

- Neighborhood infrastructure improvements project on island in Jupiter Inlet Colony, Florida. Project included over 39,000 LF of water main, gravity sewer force main, and drainage from 4" to 30" in diameter. New lift station was also installed. Project also included over 33,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales.

Broward County - North County Neighborhood Improvements Bid Pack # 11 - 2011 - 2014

Contract Amount: \$17,807,186.

- Project included over 188,000 LF of new drainage, water main, gravity sewer main, force main, reclaimed water main from 4" to 48" in diameter. Over 124,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

Palm Beach County Water Utilities Department – Belvedere Homes Phase 2 - 2012-2013

Contract Amount: \$ 4,252,998.

- Over 24,000 LF of new drainage, water main, and vacuum sewer main from 4" to 42" in diameter. Project also included 1" milling and overlay as well as over 16,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

Broward County - Utility Analysis Zone Improvement Program (UAZ) 308 - 2011-2013

Contract Amount: \$6,488,292.

- Project included over 50,000 LF of new water main, gravity sewer main, and force main from 6” to 10” in diameter. Over 50,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

Broward County – Broadview Park Neighborhood Improvement Project – Bid Pack #3 - 2010 - 2013

Contract Amount: \$13,261,559.

- Project included over 72,000 LF of new drainage, gravity sewer main, and force main from 8” to 24” in diameter. Over 150,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

LICENSES AND CERTIFICATIONS:

OSHA Qualified Person, MOT, First Aid / CPR Certified

Robert C. Henning III, Chief Estimator

1801 NW 18th STREET

POMPANO BEACH, FLORIDA 33069

Ph: 954-972-8104 Fax: 954-972-8108

bob@giannetticorp.com



Robert has over 21 years' construction experience in government and commercial construction industry as a project manager and estimator. Robert also has experience in safety program management.

EMPLOYMENT:

Giannetti Contracting Corp.	2014 –	<u>Chief Estimator</u>	2012 – 2014	<u>Project Manager</u>
Ocean Bay Construction, Inc.	2010 – 2012	<u>Project Manager / Estimator</u>		
GPE Eng. & Gen Cont., Inc.	2010	<u>Estimator</u>		
Welling Construction, Inc.	2004 – 2009	<u>President / Vice President</u>		
The Redland Company, Inc.	2003 – 2004	<u>Pro. Mgr/ Estimator/ Safety Dir.</u>	1998 – 2002	<u>Office & Field Staff</u>

RECENT PROJECTS:

City of Boca Raton, Florida – SW 18th Street Roadway Reconstruction and 16 inch Water Main Extension - 2018
Contract Amount: \$ 1,608,710.

- Roadway utility project included over 2,000 LF of new 16" water main including bridge crossing and 30" jack & bore under FEC railroad. Project included new road construction, concrete, and landscaping.

Broward County – Treasure Cove Sanitary Sewer- 2015 -2016

Contract Amount: \$2,692,515.97

- Project included over 14,700 LF of new water main and sewer main (over 15 feet deep) from 6" to 16" in diameter. 14,000 SY of roadway construction and sodded swales were also installed throughout neighborhood.

Florida Keys Aqueduct Authority – Cudjoe Inner Islands 2013 – 2016

Contract \$45,119,495.13.

- Environmentally sensitive complete sewer replacement for Cudjoe, Upper Sugarloaf, and Summerland Keys. The transmission main along US-1 is also being replaced from MM 19 to 25. Project includes over 300,000 LF of water main, low pressure force main, open cut force main, gravity sewer main, slip lining, and directional bores from 1-1/2" to 16" in diameter. Project also includes 31 area lift stations and 2 master lift stations and 200,000 SY of 1" Asphalt Overlay.

Palm Beach County Water Utilities Department – Belvedere Homes Phase 2 - 2012-2013

Contract Amount: \$ 4,252,998.

- Over 24,000 LF of new drainage, water main, and vacuum sewer main from 4" to 42" in diameter. Project also included 1" milling and overlay as well as over 16,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

Central Broward Water Control District – N-30 Canal Culvert Extension - 2012

Contract Amount: \$747,018.

- Project included clearing and installing 2,534 LF of 60" reinforced concrete pipe. Project was particularly challenging due to the extreme hard rock encountered. Averaged approximately 100 LF a day production.

Broward County - North County Neighborhood Improvements Bid Pack # 9 - 2010 -2012

Contract Amount: \$15,100,000.

- Project included over 135,000 LF of new drainage, water main, sewer main (over 15 feet deep), force main, reclaimed water main from 4" to 48" in diameter. Over 70,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

EDUCATION:

American Intercontinental University 2001-2003

Bachelor of Business Administration, January 2003 Minor in Construction Management

Broward Community College 2000-2001

Twenty-three Credit Hours towards Associate Degree in Building Construction Management

Santa Fe Community College 1998-2000

Thirty-five Credit Hours towards Associate Degree in Building Construction Management

LICENSES AND CERTIFICATIONS:

OSHA Qualified Person, Florida Stormwater Inspector, ATTSA Florida Advanced

Ilia Lyssenko, Project Manager
1801 NW 18th STREET
POMPANO BEACH, FLORIDA 33069
Ph: 954-972-8104 Fax: 954-972-8108
ilia@giannetticorp.com



Ilia has over 23 years' construction experience in government and commercial construction industry as a project manager, estimator, and foreman.

EMPLOYMENT:

Giannetti Contracting Corp.	2013 –	<u>Project Manager</u>
Lanzo Construction Co. Fla.	2010 – 2013	<u>Project Manager / Estimator</u>
DBF Construction LLC.	2006 – 2010	<u>Project Manager / Estimator</u>
Giannetti Contracting Corp.	1996 – 2006	<u>Project Manager / Estimator / Foreman</u>

RECENT PROJECTS:

City of Punta Gorda, Florida – Jones Loop Force Main - 2019

Contract Amount: \$2,066,078.44

- Large diameter force main replacement project in Punta Gorda, Florida. Project consisted of over 10,000 LF of new force main with over 90% being 16" diameter. Project also consisted on multiple 16" directional drills with four drills being over 500 LF in length. Project also consisted of a jack & bore, lift station, and associated restoration.

City of Riviera Beach, Florida – Yacht Harbor Manor Roadway Project 2017-2019

Contract Amount: \$8,642,718.50

- Neighborhood infrastructure improvements project on island in Riviera Beach, Florida. Project included over 24,700 LF of water main, gravity sewer, and drainage from 6" to 24" in diameter. Project also included over 21,000 SY of new concrete roadway construction, curbs, driveway aprons, and sodded swales.

City of Hollywood, Florida – Water Main Replacement Program – Hollywood Blvd. to Sheridan St., Federal Hwy. to Intracoastal Waterway 2015 - 2018

Contract Amount: \$12,253,900.57

- Water Main Replacement Project included over 116,000 LF of new water main and 3,400 LF of new drainage from 4" to 48" in diameter. Project also included over 217,000 SY of mill & overlay, sidewalks, driveway aprons, and sodded swales.

Loxahatchee River Environmental Control District – Jupiter Inlet Colony Neighborhood Rehabilitation Project - 2016 - 2018

Contract Amount: \$8,912,466.41

- Neighborhood infrastructure improvements project on island in Jupiter Inlet Colony, Florida. Project included over 39,000 LF of water main, gravity sewer, force main, and drainage from 4" to 30" in diameter. New lift station was also installed. Project also included over 33,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales.

Florida Keys Aqueduct Authority – Cudjoe Inner Islands 2013 – 2015

Contract \$45,119,495.13.

- Environmentally sensitive complete sewer replacement for Cudjoe, Upper Sugarloaf, and Summerland Keys. The transmission main along US-1 is also being replaced from MM 19 to 25. Project includes over 300,000 LF of water main, low pressure force main, open cut force main, gravity sewer main, slip lining, and directional bores from 1-1/2" to 16" in diameter. Project also includes 31 area lift stations and 2 master lift stations and 200,000 SY of 1" Asphalt Overlay.

EDUCATION:

Broward Community College

Associate of Arts, Engineering & Architecture

LICENSES AND CERTIFICATIONS:

Florida General Contractor, Florida Underground Contractor, Florida Plumbing Contractor
OSHA Qualified Person, Florida Stormwater Inspector, ATTSA Florida Advanced

MARC WOODWORTH, E.I.
1801 NW 18th STREET
POMPANO BEACH, FLORIDA 33069
Ph: 954-972-8104 Fax: 954-972-8108



Marc Woodworth has over 20 years' underground utility construction experience with governmental agencies as Project Manager, Construction Manager, Resident Project Representative, and Construction Inspector in - Florida.

EMPLOYMENT:

Giannetti Contracting Corp.	May 2019 – Present	Project Manager
Craven Thompson & Associates	April 1999 – May 2019	Construction Manager / RPR / Inspector
Paramount Engineering	August 1997 – April 1999	Survey Crew Party Chief, Engineer's Assist.

RECENT PROJECTS:

Broward County – Utility Analysis Zone Improvement Project (UAZ) 110 / 111 – May 2019 - Present
Contract Amount: \$25,859,999.

- Project includes 49,000 LF of new sanitary sewer main, and 64,000 LF of new water main from 4” to 24” in diameter. 160,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales where also installed throughout entire neighborhood.

Town of Davie – Eastside Phase II - 2016 – 2019
Contract Amount: \$13,638,474.

- Project included 19,000 LF of new drainage, 11,000 LF of new sanitary sewer main, and 25,000 LF of new water main from 6” to 60” in diameter. 62,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales where also installed throughout entire neighborhood.

Broward County - North County Neighborhood Improvements Bid Pack # 10 - 2012 – 2015
Contract Amount: \$11,083,453.

- Project included 15,000 LF of new drainage, 29,000 LF of new sanitary sewer main, 32,000 LF of new reclaimed water main, and 5,000 LF of new water main from 4” to 24” in diameter. 170,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales where also installed throughout entire neighborhood.

Broward County - North County Neighborhood Improvements Bid Pack # 11 - 2011 - 2014
Contract Amount: \$17,807,186.

- Project included 28,000 LF of new drainage, 42,000 LF of new sanitary sewer main, 44,000 LF of new reclaimed water main, and 45,000 LF of new water main from 4” to 18” in diameter. 124,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales where also installed throughout entire neighborhood.

Broward County - Utility Analysis Zone Improvement Program (UAZ) 308 - 2011-2013
Contract Amount: \$6,488,292.

- Project included over 50,000 LF of new water main, gravity sewer main, and force main from 6” to 10” in diameter. Over 50,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales where also installed throughout entire neighborhood.

EDUCATION:

- CLARKSON UNIVERSITY, Potsdam, NY – **BS in Civil and Environmental Engineering**

LICENSES AND CERTIFICATIONS:

Qualified Stormwater Management Inspector
E.I. – Engineering Intern

Matthew Murphy, Project Manager
1801 NW 18th STREET
POMPANO BEACH, FLORIDA 33069
Ph: 954-972-8104 Fax: 954-972-8108
matt@giannetticorp.com



Matthew has over 9 years' of construction experience with governmental and commercial construction industry as a project manager, project engineer and assistant project manager.

EMPLOYMENT:

Giannetti Contracting Corp.	2019 – Present	<u>Project Manager</u>
Greeley and Hansen	2018 – 2019	<u>Construction Engineer</u>
AECOM	2016 – 2018	<u>Project Engineer</u>
Port Morris Tile & Marble Co.	2015 – 2016	<u>Project Manager</u>
Hallen Construction	2013 – 2015	<u>Asst Project Manager & Asst Superintendent</u>
Navillus Contracting	2011 – 2013	<u>Assistant Project Manager</u>

RECENT PROJECTS:

Greeley and Hansen

Projects: City of Cape Coral North 2 Utilities Extension Project

As the Construction Engineer on the North 2 Utilities Extension Project for the City of Cape Coral, I oversaw four of the thirteen contracts across the program valuing 60 million dollars. I managed four construction inspectors who inspected contractual work for compliance with contract drawings and specifications, who in turn generated daily field reports and test results for my review. I coordinated and ran monthly progress meetings, to review individual contractors four week look ahead, contract schedule, request for information logs, change order logs and overall contract compliance. I worked closely with the client and the engineer of record to generate field orders, request for proposals and nonconformance reports. With the engineer of record, we reviewed and provided responses to the contractors request for information and submittals. After receiving responses to request for proposals, I negotiated with the contractor the value of the change in the work and review the final proposal with the client. I reviewed the individual contractors pay applications and provided the client with a suggested value of payment. I provided monthly reports to the client indicating the contractor's overall contract performance.

AECOM

Projects: CM014B – East Side Access LIRR Grand Central Terminal Concourse Facility and Fit-out

As the Project Engineer on one of the largest infrastructure projects in the United States, the LIRR Grand Central Terminal Concourse Facility and Fit-out, my responsibilities included to ensure the general contractor along with their subcontractors provide the most professional, timely and proper installation of their scope of work. I had coordinated and run startup meetings, to establish a timeframe and a sequence of work with the contractor. I reviewed monthly payment requisitions and approved for contractor payment. Inspected work performed by the contractor, to ensure they've followed contract documents, specifications and shop drawings related to the installation of the work. Reviewed Notice of Change letters to draft merit or non-merit responses. Generated punch lists for contract milestones and managed the list until completion.

Port Morris Tile & Marble Co.

Projects: Columbia University New Medical Building, Moynihan Station Phase 1, New York Presbyterian Hospital, Rudin West Village, Prudential Tower in Newark New Jersey, Long Island Welcome Center and West Point Cadet Barracks

As the Project Manager responsibilities included overseeing tile, marble & terrazzo projects from the procurement stage to completion. Closely worked with general contractors and architects to ensure completion in an efficient and timely manner. Submitted job specific submittals, schedules and samples. Assisted in estimating projects with input on production, material, manpower and duration. Attended scope review meetings for contract buyout. Managed superintendents and kept track of crew production values. Utilized timberline to keep track of purchase orders, change orders and job to date cost.

Hallen Construction

Projects: Red Oak Power Plant, Buckeye Anomaly Digs, North Queens Pipeline Test Pits, Iroquois Casing Removal and Spectra Pipeline West Side Highway Connection

As the Assistant Project Manager responsibilities included producing job specific schedules using Microsoft Project Planner while updating them monthly. Completing daily reports and logs for construction projects overseen. Created job related shop drawings using AutoCad and Bluebeam. Kept track of daily job cost for monthly billing. Issued purchase orders for material and rentals necessary for job completion. Put in weekly one call's for utility mark outs. Provided daily timesheets for workers stationed on construction project.

Navillus Contracting

Projects: JHS 157 Queens, Stuyvesant High School, Bread & Roses High School and PS 19 Queens.

As the Assistant Project Manager responsibilities included putting together submittal packages which follow specification and contract drawings issued to each project. Completing daily reports and daily logs for the construction projects overseen. Issuing purchase orders to manufacturer's in-regards to material needed for job completion. Using timberline to enter submittals, transmittals, and change issues. Up-dated project schedules for submission to project officers monthly.

EDUCATION:

POLYTECHNIC INSTITUTE OF NYU, DEPARTMENT OF CIVIL ENGINEERING, New York, NY

{This school is accredited by the Accreditation Board for Engineering and Technology}

Have earned a **BS in Civil Engineering**

LICENSES AND CERTIFICATIONS:

Certified Construction Manager ID #10124 {Certification issued by CMCI sponsored by CMAA}

Have successfully completed a 30-hour Occupational Safety and Health Training Course in Construction Safety & Health

Have successfully completed a 8-hour Lead Hazard Awareness Training Course

Have successfully completed a 4-day course with the FMI PMA

Have successfully completed Florida Department of Transportation Approved Temporary Traffic Control Advanced Course.

Tony D'Onofrio, Superintendent
1801 NW 18th STREET
POMPANO BEACH, FLORIDA 33069
Ph: 954-972-8104 Fax: 954-972-8108



Tony has over 42 years' underground utility construction experience with governmental agencies as superintendent, foreman, and operator in Michigan and Florida. Tony's experience also includes residential construction.

EMPLOYMENT:

Giannetti Contracting Corp. 1990 – Present

RECENT PROJECTS:

City of Boca Raton, Florida – SW 18th Street Roadway Reconstruction and 16 inch Water Main Extension - 2018
Contract Amount: \$ 1,608,710.

- Roadway utility project included over 2,000 LF of new 16" water main including bridge crossing and 30" jack & bore under FEC railroad. Project included new road construction, concrete, and landscaping.

City of Hollywood, Florida – Water Main Replacement Program – Hollywood Blvd. to Sheridan St., Federal Hwy. to Intracoastal Waterway 2015 - 2018

Contract Amount: \$12,253,900.57

- Water Main Replacement Project included over 116,000 LF of new water main and 3,400 LF of new drainage from 4" to 48" in diameter. Project also included over 217,000 SY of mill & overlay, sidewalks, driveway aprons, and sodded swales.

Loxahatchee River Environmental Control District – Jupiter Inlet Colony Neighborhood Rehabilitation Project - 2016 - 2018

Contract Amount: \$8,912,466.41

- Neighborhood infrastructure improvements project on island in Jupiter Inlet Colony, Florida. Project included over 39,000 LF of water main, gravity sewer force main, and drainage from 4" to 30" in diameter. New lift station was also installed. Project also included over 33,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales.

Cudjoe Regional Wastewater Inner Islands Collection System & Transmission System 2013 – 2016

Contract Amount: \$45,119,495.13.

- Project included 15,600 LF of water main, 164,625 force main and transmission main, 73,880 lf of gravity sewer, 33 sanitary lift station, 7,100 lf of 8" HDPE slip lining, 12 directional bores, 2 master lift stations, 33 dewatering wells, 572 grinder pump stations, 2 bridge crossings, trench restoration, asphalt milling and overlay.

Broward County - North County Neighborhood Improvements Bid Pack # 11 - 2011 - 2014

Contract Amount: \$17,807,186.

- Project included over 188,000 LF of new drainage, water main, gravity sewer main, force main, reclaimed water main from 4" to 48" in diameter. Over 124,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

Broward County - Utility Analysis Zone Improvement Program (UAZ) 308 - 2011-2013

Contract Amount: \$6,488,292.

- Project included over 50,000 LF of new water main, gravity sewer main, and force main from 6" to 10" in diameter. Over 50,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

Broward County – Broadview Park Neighborhood Improvement Project – Bid Pack #3 - 2010 - 2013

Contract Amount: \$13,261,559.

- Project included over 72,000 LF of new drainage, gravity sewer main, and force main from 8” to 24” in diameter. Over 150,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

Broward County – Utility Analysis Zone Improvement Program (UAZ) 307 & 315 - 2009 - 2011

Contract Amount: \$5,949,866.

- Project included over 38,000 LF of new water main, gravity sewer main, and force main from 4” to 12” in diameter. Over 36,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

Florida Keys Aqueduct Authority – Big Coppitt Wastewater Collection System Contract 2, Rockland & Geiger Key, Florida - 2008 - 2010

Contract Amount: \$9,667,750.

- Project included over 73,000 LF of new water main, gravity sewer main, and force main from 4” to 8” in diameter. Over 76,000 SY of mill & overlay, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

LICENSES AND CERTIFICATIONS:

Michigan Plumbing & Underground
Michigan Mechanical

Tim Gibbs, Superintendent
1801 NW 18th STREET
POMPANO BEACH, FLORIDA 33069
Ph: 954-972-8104 Fax: 954-972-8108



Timothy Gibbs has over 27 years' underground utility construction experience with governmental agencies as superintendent, foreman, operator, topman, tailman, pipelayer, grademan in Michigan and Florida. Tim's experience also includes residential construction.

EMPLOYMENT:

Giannetti Contracting Corp. 1997 – Present

Di Gregorio & Sons, Michigan 1992 Dimar Construction, Michigan 1994 Pamar Enterprises, Michigan 1996

RECENT PROJECTS:

City of Punta Gorda, Florida – Jones Loop Force Main - 2019

Contract Amount: \$2,066,078.44

- Large diameter force main replacement project in Punta Gorda, Florida. Project consisted of over 10,000 LF of new force main with over 90% being 16" diameter. Project also consisted on multiple 16" directional drills with four drills being over 500 LF in length. Project also consisted of a jack & bore, lift station, and associated restoration.

City of Riviera Beach, Florida – Yacht Harbor Manor Roadway Project 2017-2019

Contract Amount: \$8,642,718.50

- Neighborhood infrastructure improvements project on island in Riviera Beach, Florida. Project included over 24,700 LF of water main, gravity sewer, and drainage from 6" to 24" in diameter. Project also included over 21,000 SY of new concrete roadway construction, curbs, driveway aprons, and sodded swales.

Loxahatchee River Environmental Control District – Jupiter Inlet Colony Neighborhood Rehabilitation Project - 2016 - 2018

Contract Amount: \$8,912,466.41

- Neighborhood infrastructure improvements project on island in Jupiter Inlet Colony, Florida. Project included over 39,000 LF of water main, gravity sewer force main, and drainage from 4" to 30" in diameter. New lift station was also installed. Project also included over 33,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales.

Cudjoe Regional Wastewater Inner Islands Collection System & Transmission System 2013 – 2016

Contract Amount: \$45,119,495.13.

- Project included 15,600 LF of water main, 164,625 force main and transmission main, 73,880 lf of gravity sewer, 33 sanitary lift station, 7,100 lf of 8" HDPE slip lining, 12 directional bores, 2 master lift stations, 33 dewatering wells, 572 grinder pump stations, 2 bridge crossings, trench restoration, asphalt milling and overly

Broward County - North County Neighborhood Improvements Bid Pack # 11 - 2011 - 2014

Contract Amount: \$17,807,186.

- Project included over 188,000 LF of new drainage, water main, gravity sewer main, force main, reclaimed water main from 4" to 48" in diameter. Over 124,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

Broward County - Utility Analysis Zone Improvement Program (UAZ) 308 - 2011-2013

Contract Amount: \$6,488,292.

- Project included over 50,000 LF of new water main, gravity sewer main, and force main from 6" to 10" in diameter. Over 50,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

Broward County – Broadview Park Neighborhood Improvement Project – Bid Pack #3 - 2010 - 2013

Contract Amount: \$13,261,559.

- Project included over 72,000 LF of new drainage, gravity sewer main, and force main from 8" to 24" in diameter. Over 150,000 SY of new roadway construction, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

Florida Keys Aqueduct Authority – Big Coppitt Wastewater Collection System Contract 2, Rockland & Geiger Key, Florida - 2008 – 2010

Contract Amount: \$9,667,750.

- Project included over 73,000 LF of new water main, gravity sewer main, and force main from 4" to 8" in diameter. Over 76,000 SY of mill & overlay, sidewalks, driveway aprons, and sodded swales were also installed throughout entire neighborhood.

LICENSES AND CERTIFICATIONS:

OSHA Qualified Person, First Aid / CPR Certified



Labor Force

Officers – 2 EA

Office Staff – 12 EA

Project Managers – 4 EA

Superintendents – 5 EA

Foreman – 8 EA

Operators – 16 EA

Pipe Layers – 5 EA

Laborers – 28 EA

Mechanics/Yard – 6 EA

Truck Drivers – 6 EA

Total: 92 EA



Giannetti Contracting Corporation
Equipment List

Articulated Truck - Cat D250E - 1997	#5TN00947
Asphalt Zipper AZ500B	#50000445
Asphalt Zipper AZ360b	#AZ-0169
Asphalt Mill - Cat 2014 PM-102	#Z2X00572
Asphalt Paver - Cat 2013 AP255E	#D8A00175
Asphalt Roller - CAT CB24B	#42000227
Backhoe 480F Case	#JJG0004055
Backhoe CAT 420F	#JWJ001135
Dozer - Cat D5XLHST	#7PS01973
Excavator-John Deere 50G Compact Exc.	#FF050GXTTHH286332
Excavator-Volvo EC140EL	#310326
Excavator-Volvo EC220EL	#310351
Excavator-Takeuchi TB210	#211001709
Excavator- TB290CR w/Attach.	#185102405
Excavator- TB290CR w/Attach.	#185103026
Excavator-328 Mini Bobcat	#234211270
Excavator - Cat 307	#2PM00781
Excavator - Cat 321	#MPG00522
Excavator - Cat 328	#RMX00508
Excavator - Cat 365CL	#MCS00247
Excavator - Komatsu PC308	#30190
Skidsteer - Cat 262D W/Bucket	#DTB01656
Skidsteer - Cat 242D	#DZT00400
Planer PC306B (For above skidsteer)	#PCT00507
Loader - J. Deere 524K	#1DW524KZCGF677568
Loader - J. Deere 524KII 4WD	#1DW524KZVHF685253
Loader - J. Deere 524K	#1DW524KZCGF678574
Loader - Cat 950G 2003	#8950GVBA00262
Loader - Cat 906 2005	#00906AMER00551
Loader - Cat 924K	#PWR02796
Loader - Komatsu WA200/6	#71455
Loader - Komatsu WA200/6	#70758
Loader - Komatsu WA270/7	#K47109
Loader - Cat 924G	#DDA03809
Loader - Volvo BL60B - 2012	#VCE0BN60BH02121415
John Deere Broom Tractor 4520	#LV4520H340397
Laser - Dialgrade - Pipe Laser	#10699
Javlin Dual Slope Laser	#2069
Roller-Cat Vibr. Smooth Drum CS433E	#CFP00141

Roller - Ingersoll Rand SD40D	#5778
Deutz Solar Arrow Board	
Boring Machine - Richmond 30"	#5172238
Miscellaneous Supplies	
12" Rotary Wellpoint Pump	#V933
12" Rotary Wellpoint Pump	#V904
12" Rotary Wellpoint Pump (Quiet)	#V923
12" Rotary Wellpoint Pump (Quiet)	#V1080
10" Wellpoint Atlantic Duetz Diesel	
Bobcat Sweeper Attachment	#NA
Bobcat Trencher Attachment	#NA
Bobcat Trencher	#045-40505437
Trencher - Vermeer V8550A 1999	#1VRT112P2X1000225
Cat Broom for Skid Steer Loader	#1425455
Cat Sideshift Trencher	#JAJ04479
Bobcat Mill Attachment	#NA
81 GMC Tool Truck	#2945
Gallion Grader A550	#GC-10349
Cat 36 KW Generator	#16MPF08YD027597
Cat 25 KW Generator	#7201133
3 - 8" Hydraulic Pumps	
Mauldin Tack Tank MT300	#Y02912
2003 Terramite TSS38 Ride On Broom	#23TS0435
2012 Rammex 1510CI Trench Comp.	#60387
2000 case Forklift	#589E
Tractor W/Broom - John Deere 4520	#LV4520H440256
Paver 8500 - Lee Boy	#0652195011572
9cu Ft. Concrete Mixer 2015	#C1552172
G440 Motor Grader - 1987 Lee Boy	#87-194

**CONSENT RESOLUTION
OF THE SHAREHOLDERS, OFFICERS AND DIRECTORS OF
GIANNETTI CONTRACTING CORPORATION**

The undersigned, being all the Shareholders, Officers and Directors of Giannetti Contracting Corporation, a Florida corporation (the "Company") do hereby, by this Consent Resolution, adopt the following resolutions, hereby waiving notice and call of a meeting therefore, to wit:

WHEREAS, Giannetti Contracting Corporation during the course of its business operations is required to submit prequalification bid packages and bid proposals to various municipalities, owners, and prospective customers;

WHEREAS, Giannetti Contracting Corporation needs an authorized signatory in order to submit prequalification bid packages and actual bid packages, as part of its ongoing business operations;

WHEREAS, the Shareholders, Officers and Directors of Giannetti Contracting Corporation, desire to set forth the individuals who are authorized to sign any bid qualification packages and actual bids to various owners;

IT IS HEREBY RESOLVED, that the Shareholders, Officers and Directors of the Company hereby consent and approve the following individuals, as authorized signatory representatives, to sign any pre-qualification bid packages and actual bids, on behalf of Giannetti Contracting Corporation. The individuals authorized are as follows:


Richard Gibbs III	President / Treasurer
Nicholas Apostol	Vice President / Secretary
Jeffery Melnechuk	Authorized Signatory

IT IS HEREBY FURTHER RESOLVED, that any of the authorized representatives identified above are hereby authorized and directed to execute all documents, instruments or papers necessary to effectuate any prequalification bid packages and/or actual bid packages, on behalf of Giannetti Contracting Corporation.


IT IS HEREBY FURTHER RESOLVED, that the Shareholders Officer and Directors hereby affirm, ratify and consent to all actions to be taken, agreements to be executed, documents to be delivered by Giannetti Contracting Corporation, as it relates to prequalification bid packages and actual bid packages to various owners.

*****SIGNATURES ON FOLLOWING PAGE*****

IN WITNESS WHEREOF, the undersigned being the all of the Shareholders, Officers and Directors of Giannetti Contracting Corporation do hereby declare that the actions taken by the foregoing resolutions are in the best interest of Giannetti Contracting Corporation and that they have executed this Consent Resolution as of this 3rd of January, 2018.



By: Richard Gibbs III,
Its: Shareholder, Officer and Director



By: Nicholas Apostol
Its: Shareholder, Officer and Director



By: Angelina Giannetti, Director and Co-Trustee
of the Ricky L. Giannetti Family Trust,
Dated August 1, 2006
Its: Shareholder and Director
